



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 11/10/2021

Weather: 52 degrees. Rain. High of 54 degrees today.

Hours Worked: 11/10/2021 - 09:00 – 15:00hrs (6hrs) Site Visit, Progress Meeting,
11/09/2021 – 06:30 – 07:00hrs (0.5) Site Visit to verify Material billed in October Pay App was present on site.
11/08/2021 – 16:00 – 16:30hrs (0.5hrs) Reviewed Pay App for October.
11/04/2021 – 11:00 – 12:30hrs (1.5hrs) Received Call from Todd advising that he needed me on site to verify spongy soil in the North east corner of Student Parking Lot. Hillis-Carnes on Site during Proof Roll of Parking Lot.

Beuchert Excavation: Four (4) men are on site today working on the North side of the School main Driveway.

Industrial Concrete: One (1) man is on site chipping concrete and cleaning around Diamonds that are sitting high.

J.D. Long, Masons: They have a few men on site touching up block and repairing damaged walls.

Hazzard Electric: Eleven (12) men are on site.

Colonial Webb: Thirteen (13) men are on site today.

Talley & Armstrong (Sub-Contractor of Beuchert): They are pouring Mowing strips on the West side of Area B and Pouring concrete at the Loading Dock.

Weldon Steel: I did not observe anyone on site.

JP Construction: Fourteen (14) men are on site today.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: Three (3) men were on site today. They continue to set frames and glass in various locations.

United Sprinkler: One (1) man on site. Working on Sprinkler System in various areas.

CTSI: Five (5) men are on site and are pulling low voltage wiring.

M. L. Straight: Four (4) men are on site Painting in Area A.

K-Plus: No one is on site.

AAM: Four (4) are on site. They are installing Metal Panels.

Hodgemen: Two (2) men are laying wall tile in Area A.

Deleware Elevator: No one was on site during either visit.

S&S Concrete Cutting Company: Two (2) men are on site today. Coring Walls.

DES: Three (3) men are on site. Installing Casework in various locations.

Smith: Two (2) men on site pouring epoxy floors.

TJ Distributers, INC: No one was on site yesterday or today.

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe anyone on site during my visits.

Conversations with Branch Builds: I went by the site this morning 11/10/2021 specifically to meet with Todd to discuss questions I had on the Pay Application for October. Todd was meeting with Sub-Contractor on site and therefore I was unable to meet with him. I walked the site and observed the work that has been completed since my last visit and also the work that was underway. I then attended the 11:00hrs Progress Meeting with Alexes and Deborah in the County's Conference Room. After the meeting I went back to the Construction Site to meet with Todd to review the Pay Application. While I was waiting to meet with Todd, Dr. Perry and Ralph Fallin arrived on site. Dr. Perry Ralph and I spoke about the Project and the cost of the change to the Bio Pond on the North East corner of the site.

I met with Todd at approximately 13:15hrs and we reviewed the Pay Application for October. After some discussion, Todd agreed to remove the Labor for the installation of Plumbing Fixtures. All other items that I had questions about were satisfied.

After my meeting with Todd I again walked the site and spent some time catching up on emails related to the School.

Finally, Napier a sub-Contractor for Atlantic Broadband was on site on 11/11/2021 boring under Rt.#3 so that Atlantic Broadband could complete their work. I notified Todd and Dr. Perry of their presence.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. DEQ has scheduled a visit for November 15, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report -

Hillis-Carnes Grout Inspection/Compression Strength Test – 11/02/2021

Hillis-Carnes Field Reports – 11/04/2021, 11/08/2021, 11/09/2021

Hillis-Carnes Bio Retention Pond Reports –

Submittals – #10 11 25-1.1, #11 00 05-8.0, #11 52 13-5.1, #28 16 00-3.0, #26 24 16-2.0, #11 00 05-7.0, #33 40 00-5.0

RFIs – #308, #325, #331, #332, #333, #338, #339, #340, #342, #346

Patrick Byrne – WLHS – Parking Lot Undercut and Bridging Work, 11/12/2021 Open PCO's

Tara Delaney – Approval of Change Order #12.

Change Order/PCOs/Pay App – #64

Weekly Submittal Status Report: 11/05/2021, 11/12/2021

Weekly RFI Status Update – 11/05/2021, 11/12/2021

Weekly Daily Log Summary – 11/05/2021, 11/12/2021

PCO Log – 11/05/2021, 11/12/2021



Photo 1 - Plants stage to be planted in Bio-pond located on the Northwest Corner of the site.



Photo 2 - Tress staged to be planted in front of the School.



Photo 3 - Holes dug for trees.

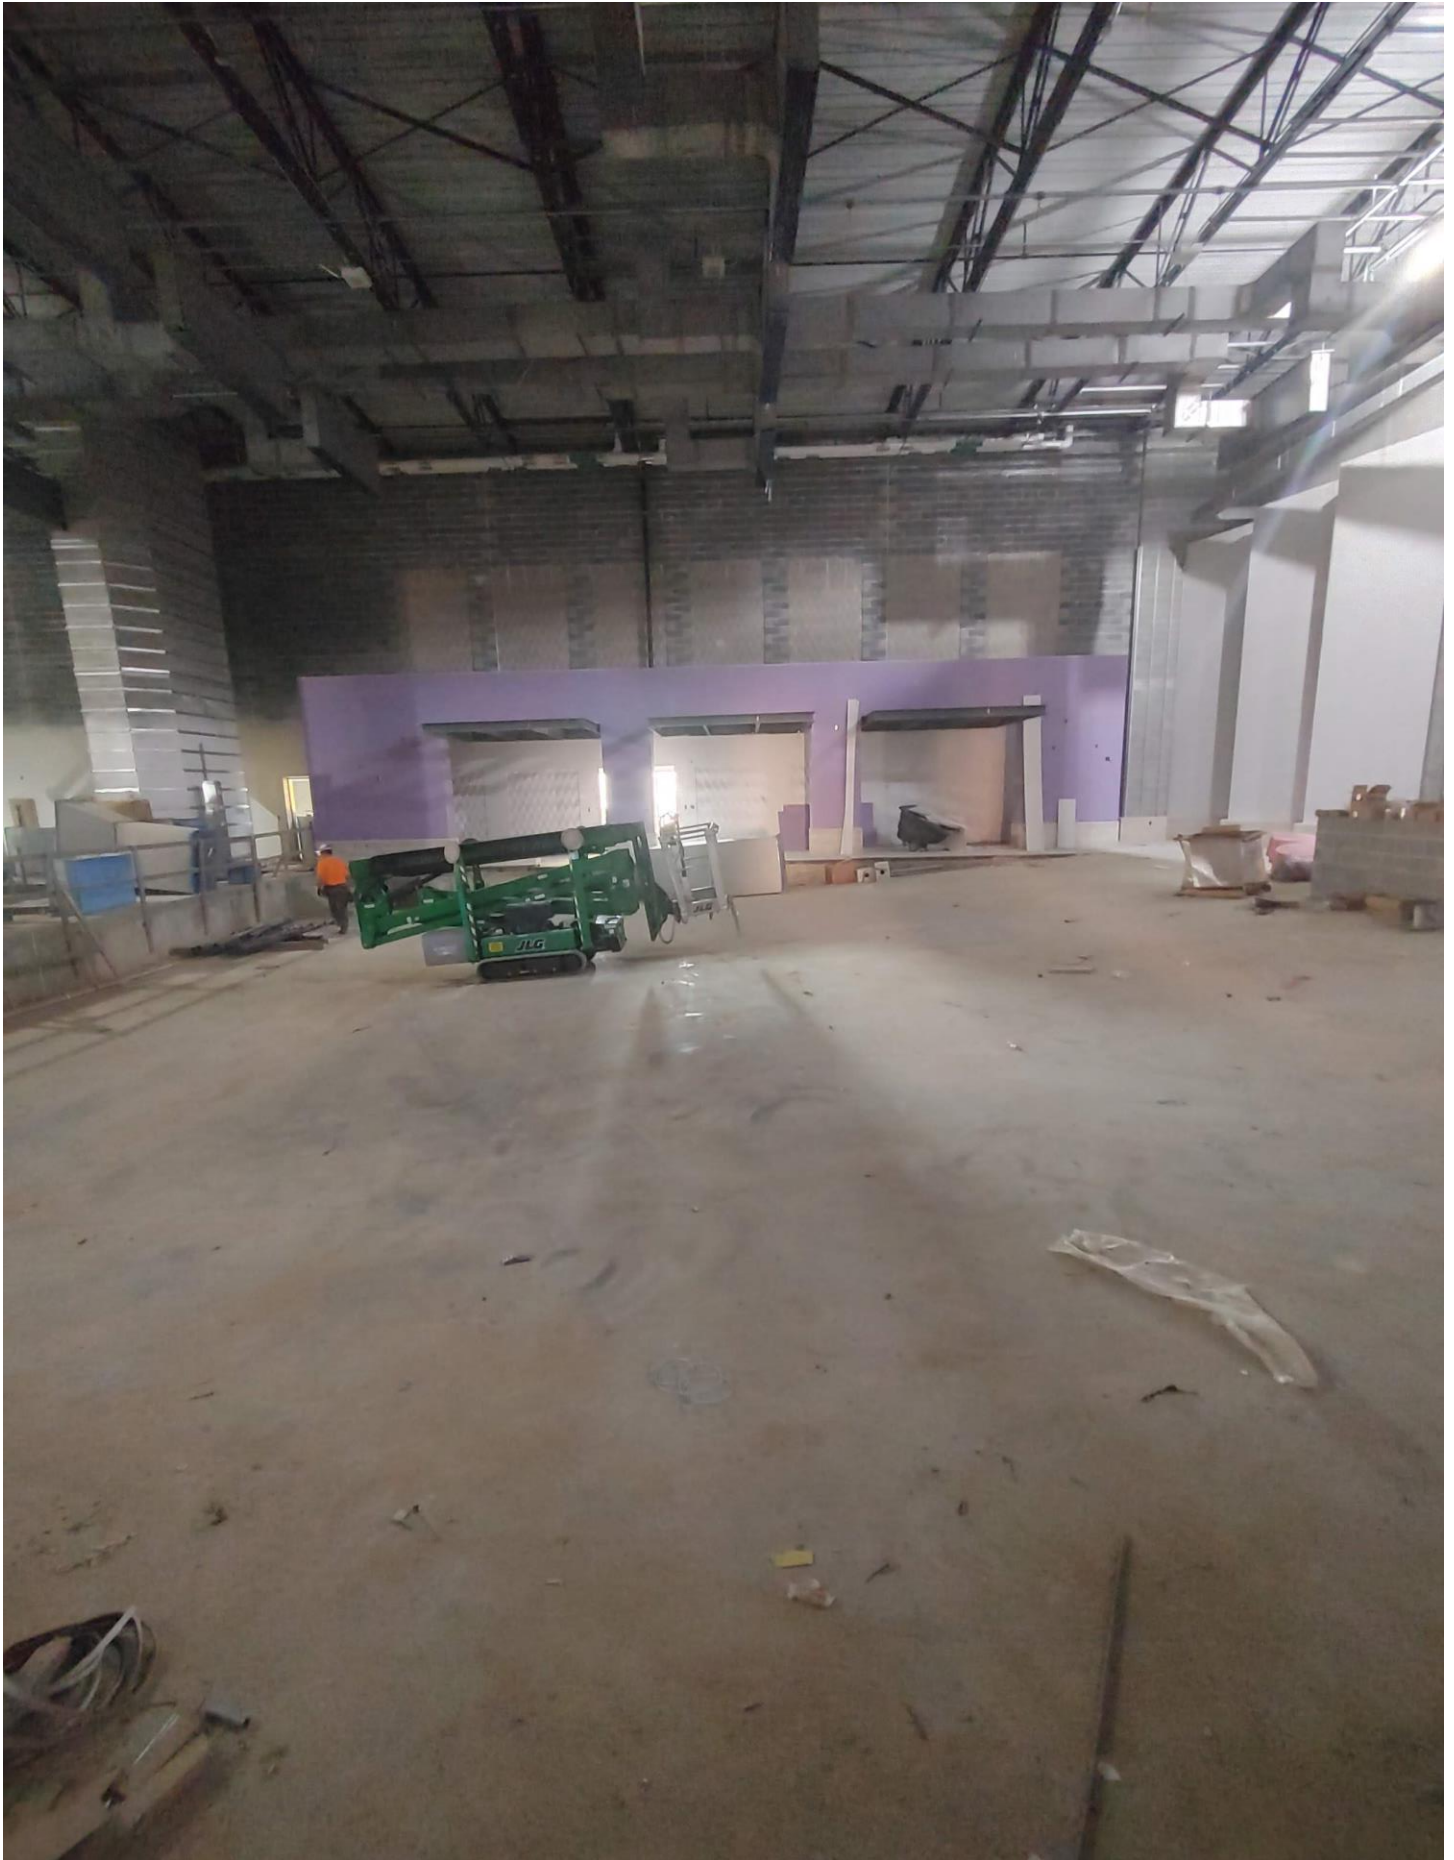


Photo 4 - Sheetrock is being hung in the Auditorium

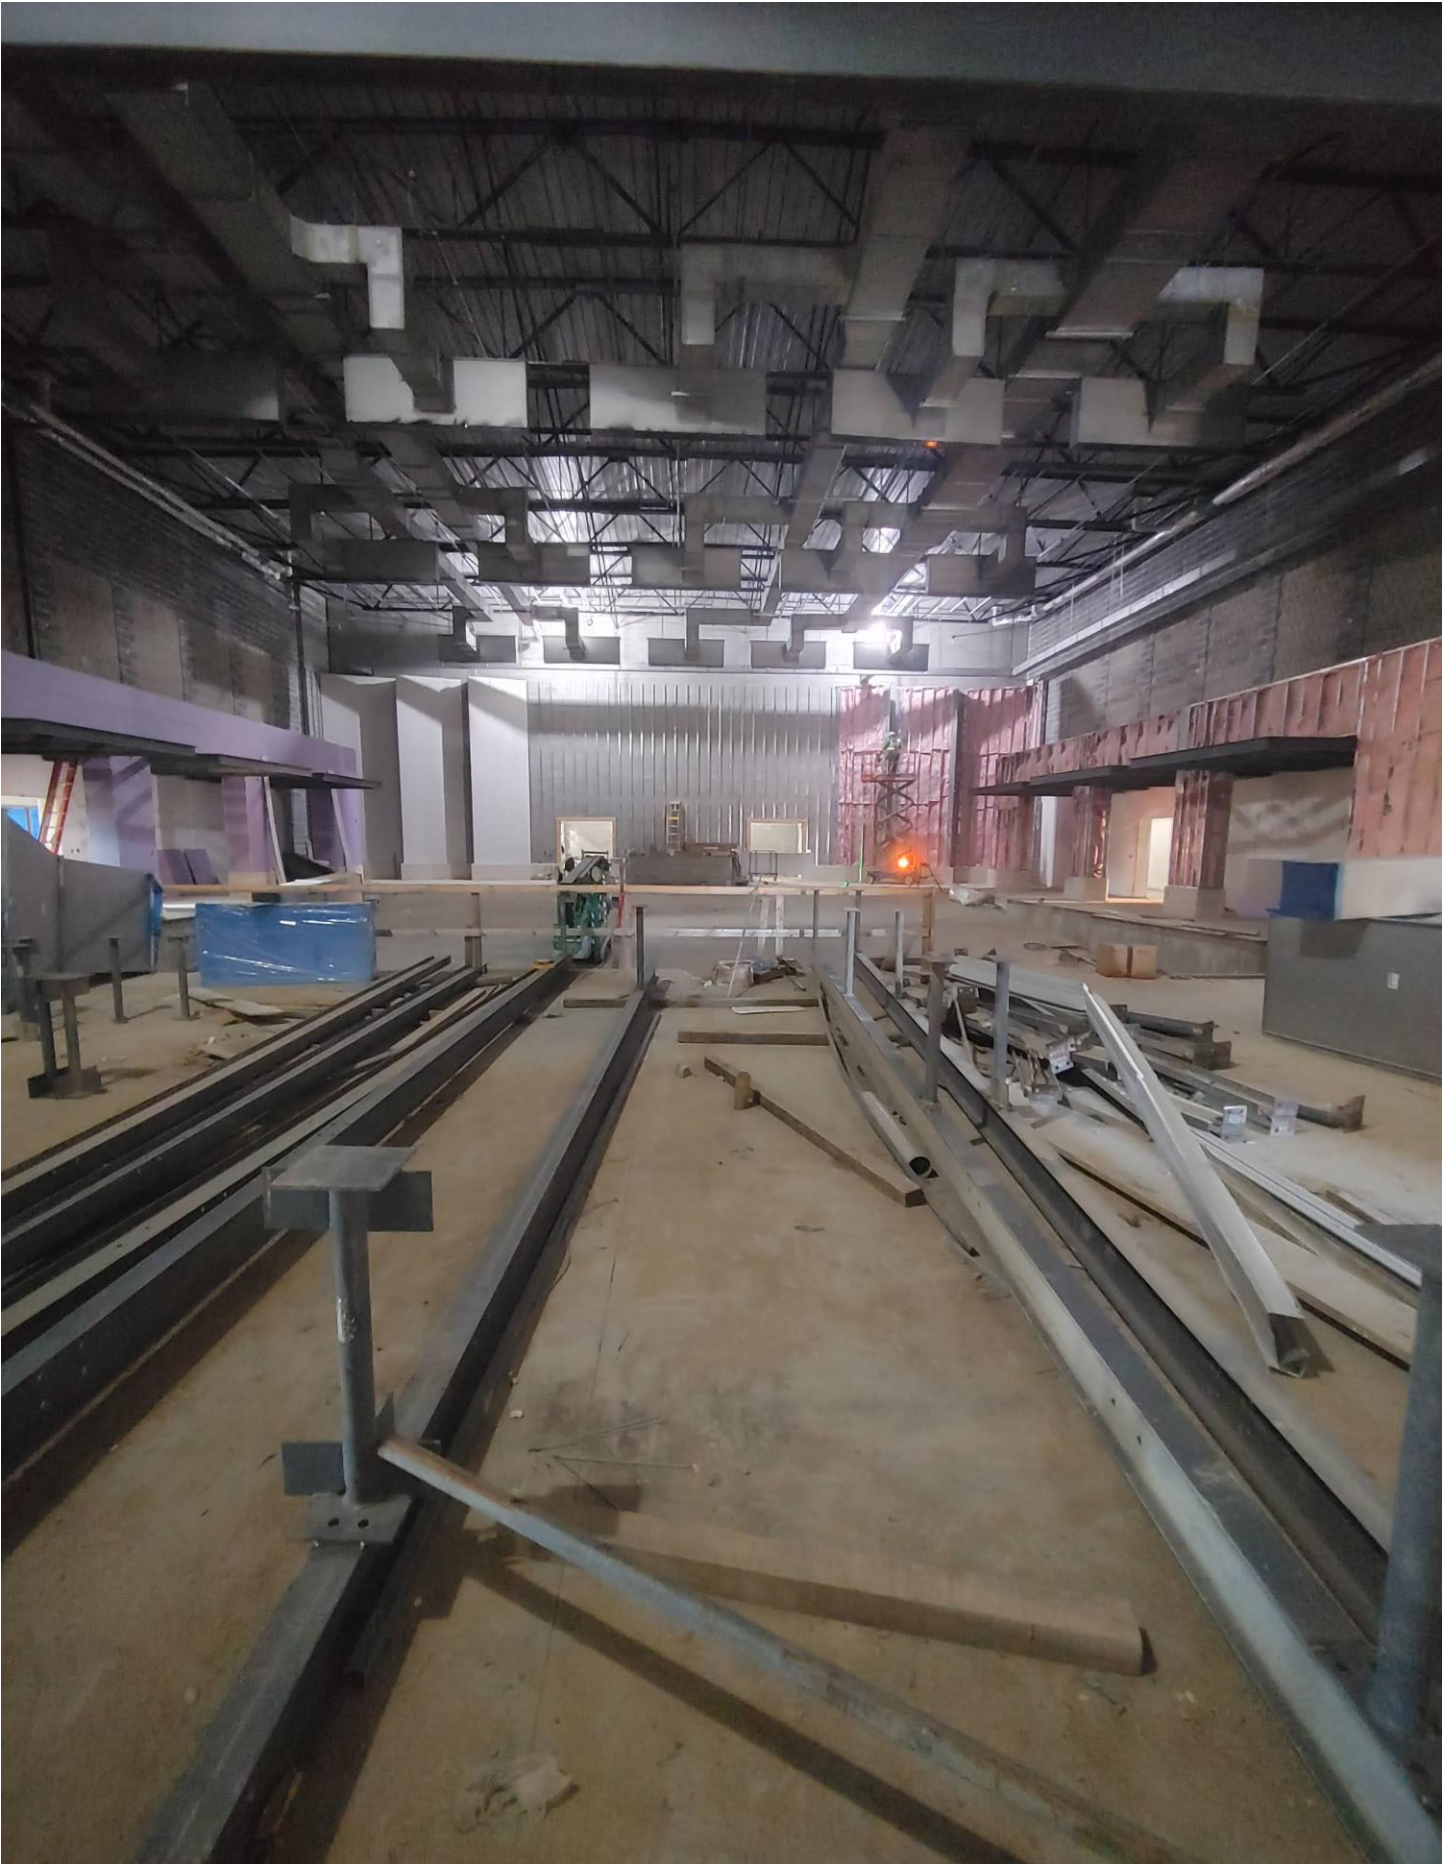


Photo 5 - Sheetrock is being hung on the West wall of the Auditorium.

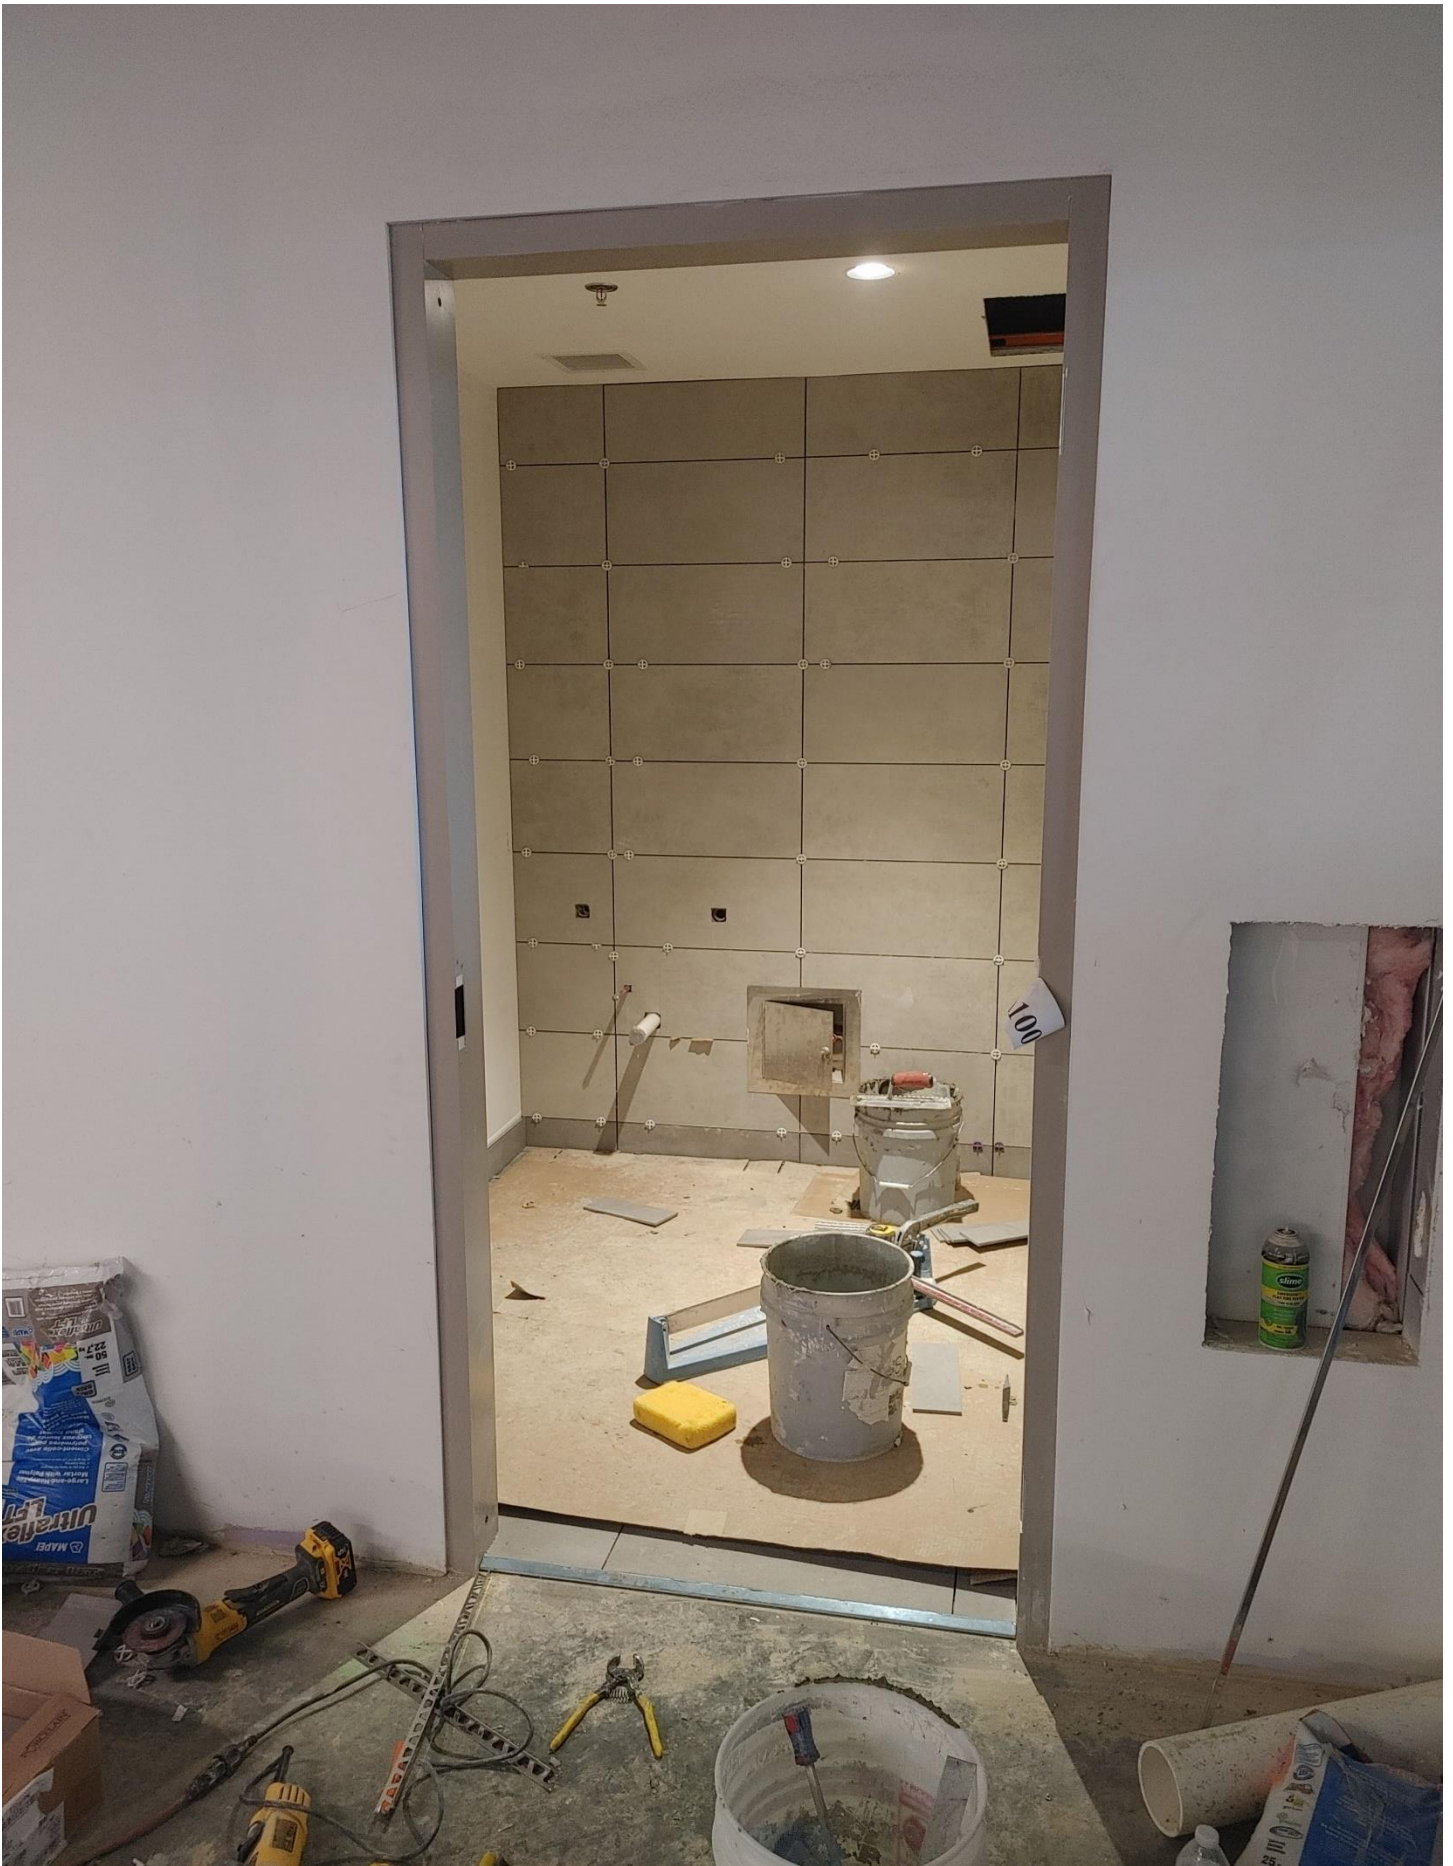


Photo 6 - Wall tile is being laid in Area A.



Photo 7 - Progress is being made on the Student Parking lot.



Photo 8 - Front of the site.



Photo 9 - Ship Ladders are being set on the roof.



Photo 10 - Bus Loop area

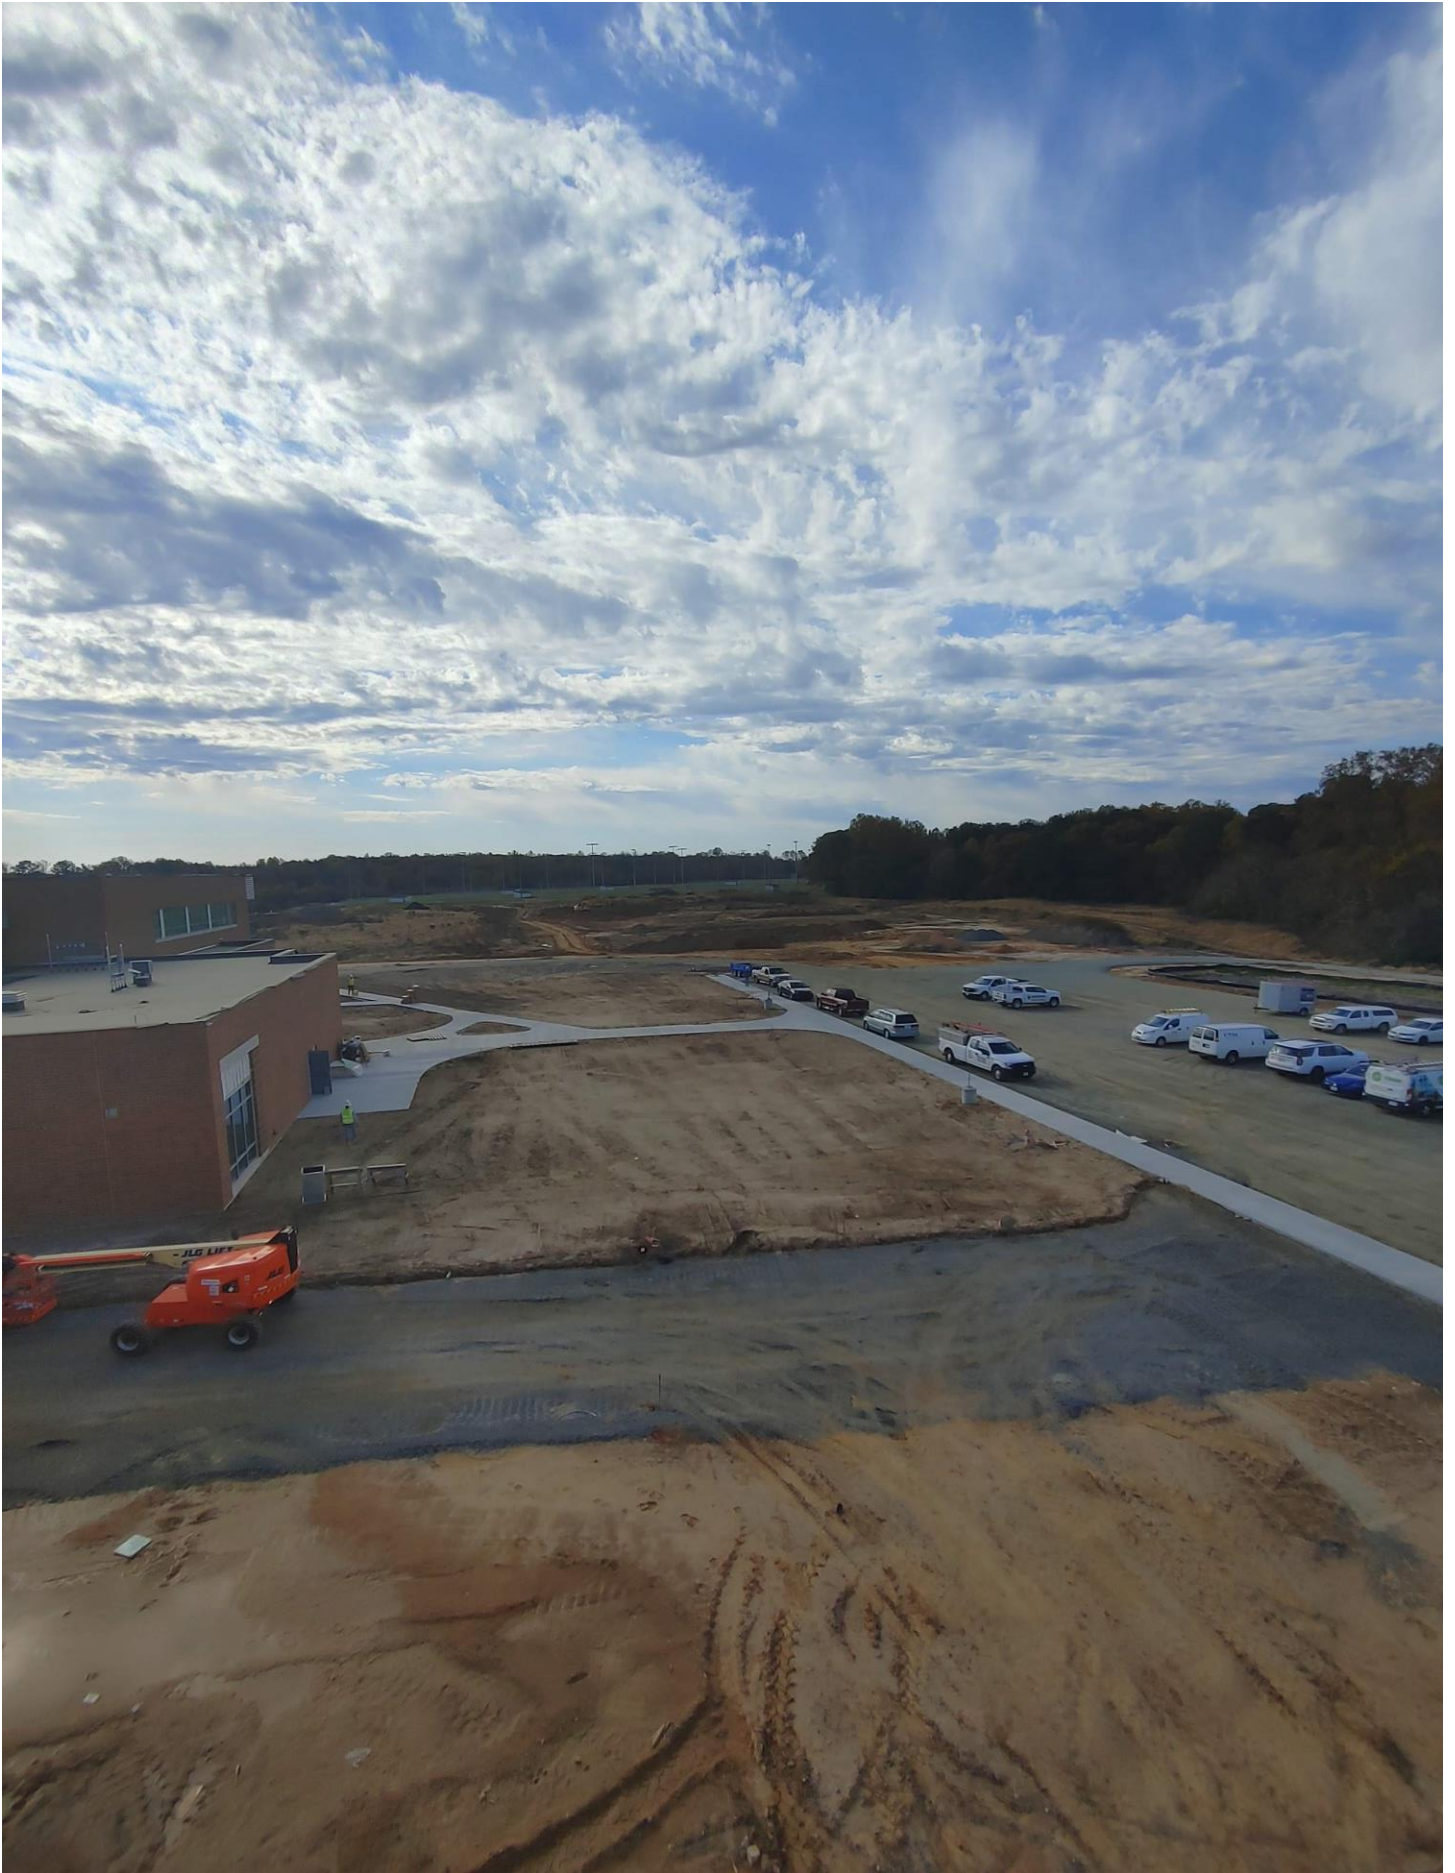


Photo 11 - West side of the site.



Photo 12 - Concrete is being poured in the Loading Dock Area
