



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 11/19/2021

Weather: 47 degrees. Sunny. High of 50 degrees today.

Hours Worked: 11/10/2021 – 10:30 – 13:30hrs (3hrs) Site Visit. I also went by Alexes Lee's Office and signed October's Pay Application. I am taking Vacation next week and therefore there will not visit the site.

Beuchert Excavation: Is on site today working on the East side of the School.

Industrial Concrete: I did not observe them on site during my visit.

J.D. Long, Masons: No one is on site today.

Hazzard Electric: They are on site working in various areas around the site.

Colonial Webb: I did not observe anyone on site today during my visit.

Talley & Armstrong (Sub-Contractor of Beuchert): They are pouring concrete at the Loading Dock.

Weldon Steel: I did not observe anyone on site.

JP Construction: I did not observe anyone on site.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: They are working on setting SF49B in Area C.

United Sprinkler: Two (2) men are site. Working on Sprinkler System in Area C.

CTSI: They are on site and are pulling low voltage wiring.

M. L. Straight: I did not observe anyone on site.

K-Plus: Is on site Caulking in various areas..

AAM: They are installing Metal Panels on the West side of Area C.

Hodgemen: I did not observe anyone on site during my visit.

Deleware Elevator: No one was on site during either visit.

S&S Concrete Cutting Company: No one is on site today.

DES: I did not see anyone on site today.

Smith: No one is on site to my knowledge.

TJ Distributers, INC: No one was observed on site during my visit

Linear Surveyors: No one is on site today.

Hillis-Carnes: Has a Tech on site sampling and testing concrete that was being poured at the Loading Dock.

Conversations with Branch Builds: I met with Cooper on site and received an update on what is or has been happening. Cooper said that they are close to resolving the Cap/flashing on the Parapet walls and the Sub is ready to start once everything has received final approval. He said that they plan on pouring concrete on the South side of Area C on Monday. Some of the Grand Staircase has been erected. I asked when the rest was going to be completed. Cooper said they are waiting for the Sub who is installing the wood tread to come out and measure and inspect what has been done thus far. Once that visit occurs they will finish setting the rest of the Staircase.

Atlantic Broadband is on site pulling cable through the underground conduit installed by Branch.

I received a call on Tuesday, November 16th from John - Branch Builds inquiring the status of the completion of the Sewage Pump Station. I told John that Franklin Mechanical should be on site working but that they still needed the electrical portion completed by Hazzard Electric. I told John I would verify that Franklin Mechanical was on site and get back to him. I verify they were on site and let John know.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on June 7, 2021 at 09:00hrs. DEQ has re-scheduled their November 15, 2021 at 09:00hrs to November 29, 2021 at 09:00hrs.

Reviewed emails:

Hillis-Carnes Concrete Break Report - 11/18/2021

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports – 11/11/2021, 11/12/2021, 11/13/2021, 11/16/2021, 11/17/2021, email from Jennifer Melton on 11/18/2021 Outline of unresolved items.

Hillis-Carnes Bio Retention Pond Reports –

Submittals – #11 52 13-5.1

RFIs –

Patrick Byrne – 11/12/2021 Open PCO's

Tara Delaney –

Change Order/PCOs/Pay App – PR #3

Weekly Submittal Status Report: 11/19/2021

Weekly RFI Status Update – 11/19/2021

Weekly Daily Log Summary – 11/19/2021
PCO Log – 11/19/2021



Photo 1 Sidewalks in the Student Parking Lot area have been poured



Photo 2 - Trees have been planted



Photo 3 - Trees have been planted in front of Area A



Photo 4 - Shrubs have been planted in Bio-Pond



Photo 5 - Shrubs and Trees have been planted in Bio Pond



Photo 6 - Trees have been planted around Bio Pond on West side of the site.



Photo 7 - West side of site



Photo 8 - Some of the Concrete has been poured on the South side of Area C. Remainder scheduled to be poured on Monday



Photo 9 - Concrete forms are being erected on the South side of Area D.



Photo 10 - XD08 Overhead roll-up door has been installed



Photo 11 - Preparing to pour the remaining section of the Loading Dock and steps.



Photo 12 - The erection of the Grand Staircase has begun.

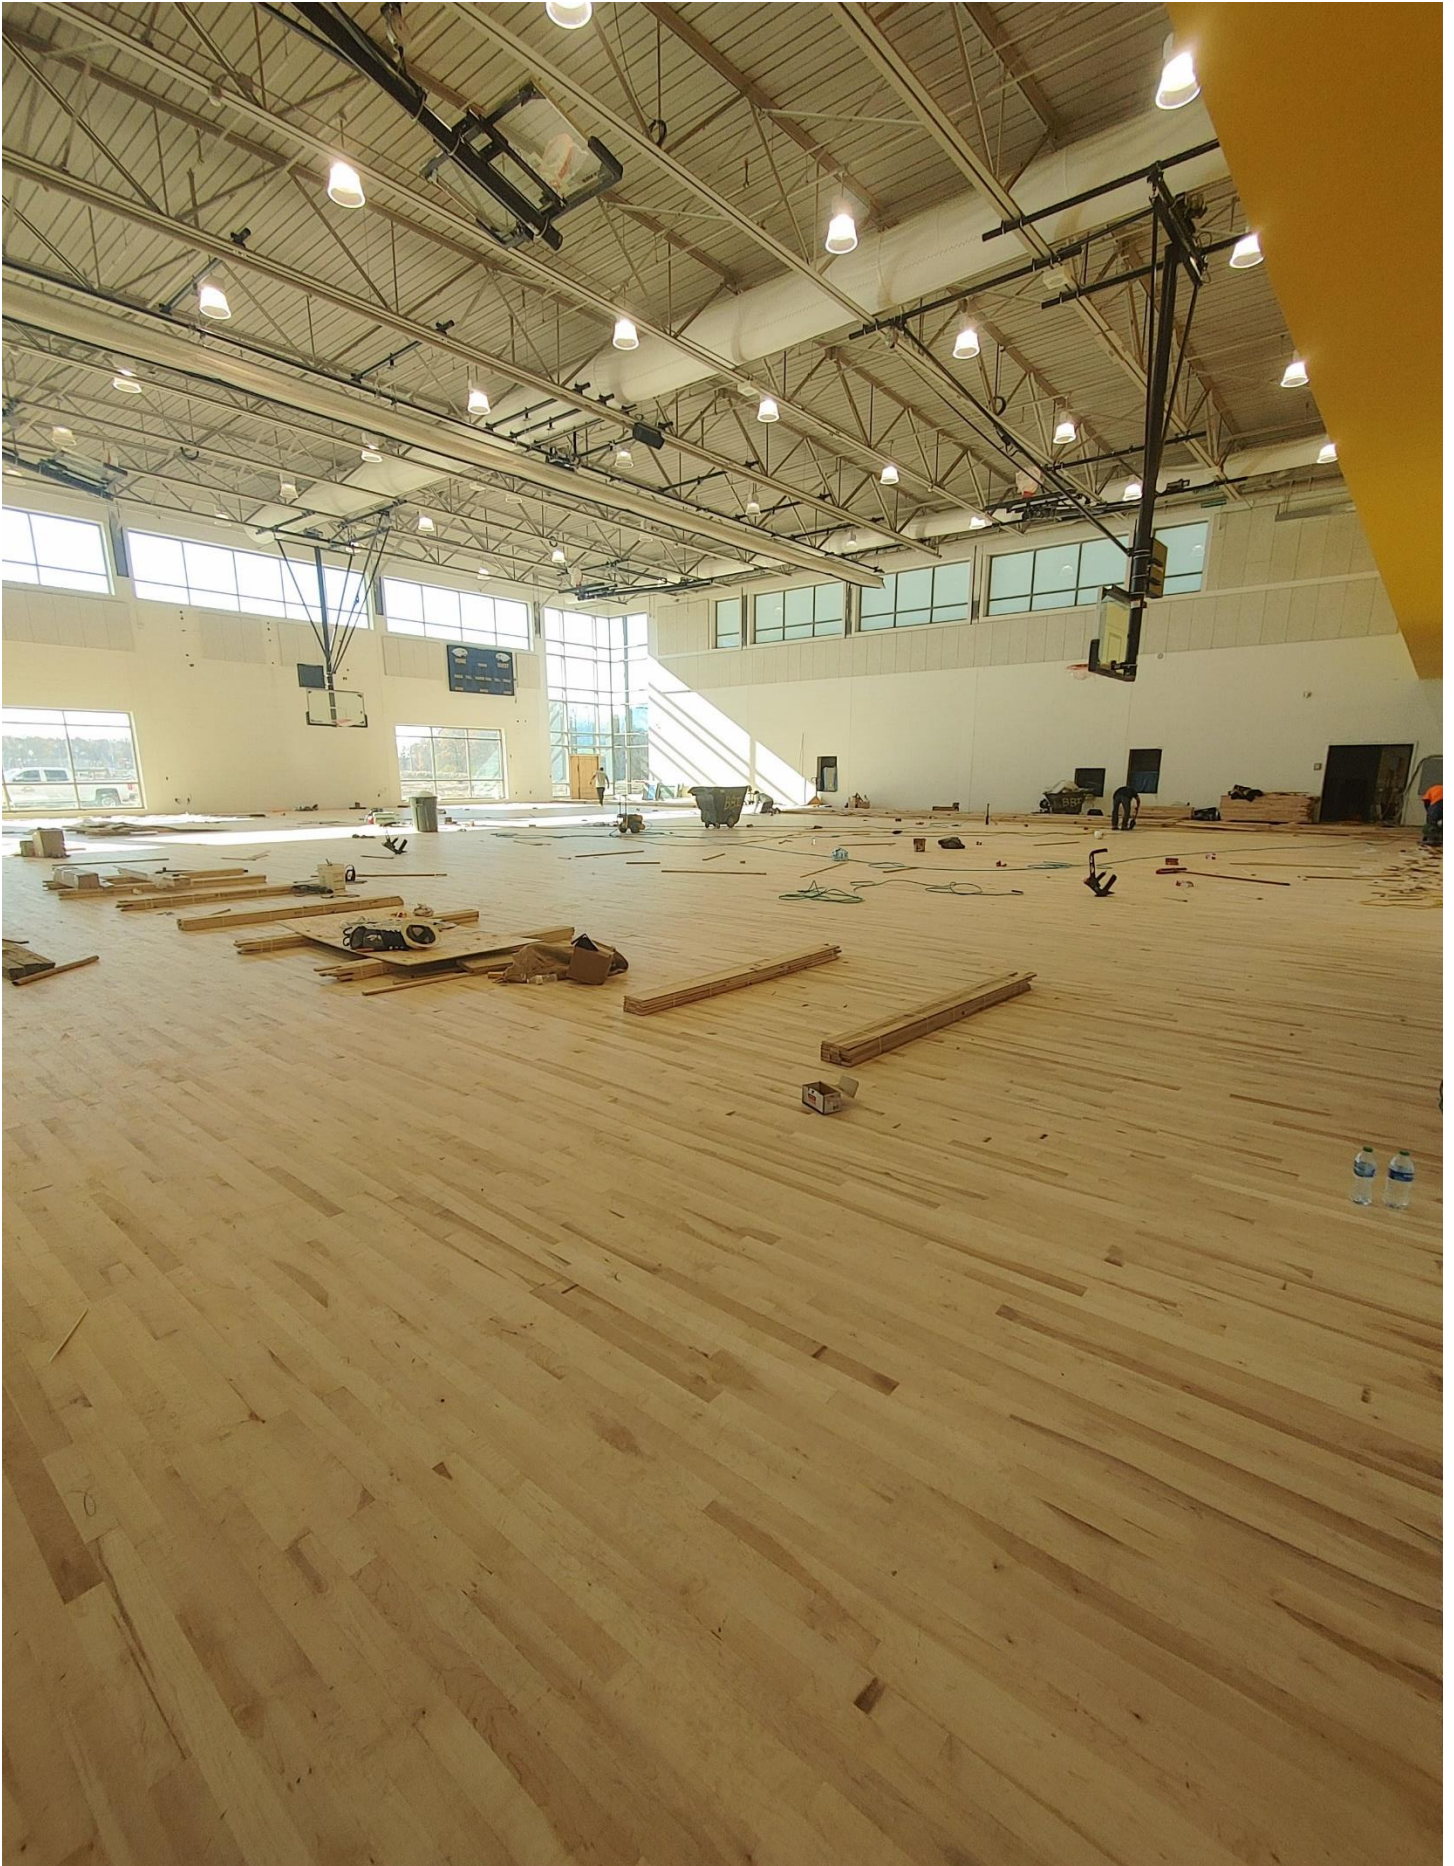


Photo 13 - Gym Floor is being installed

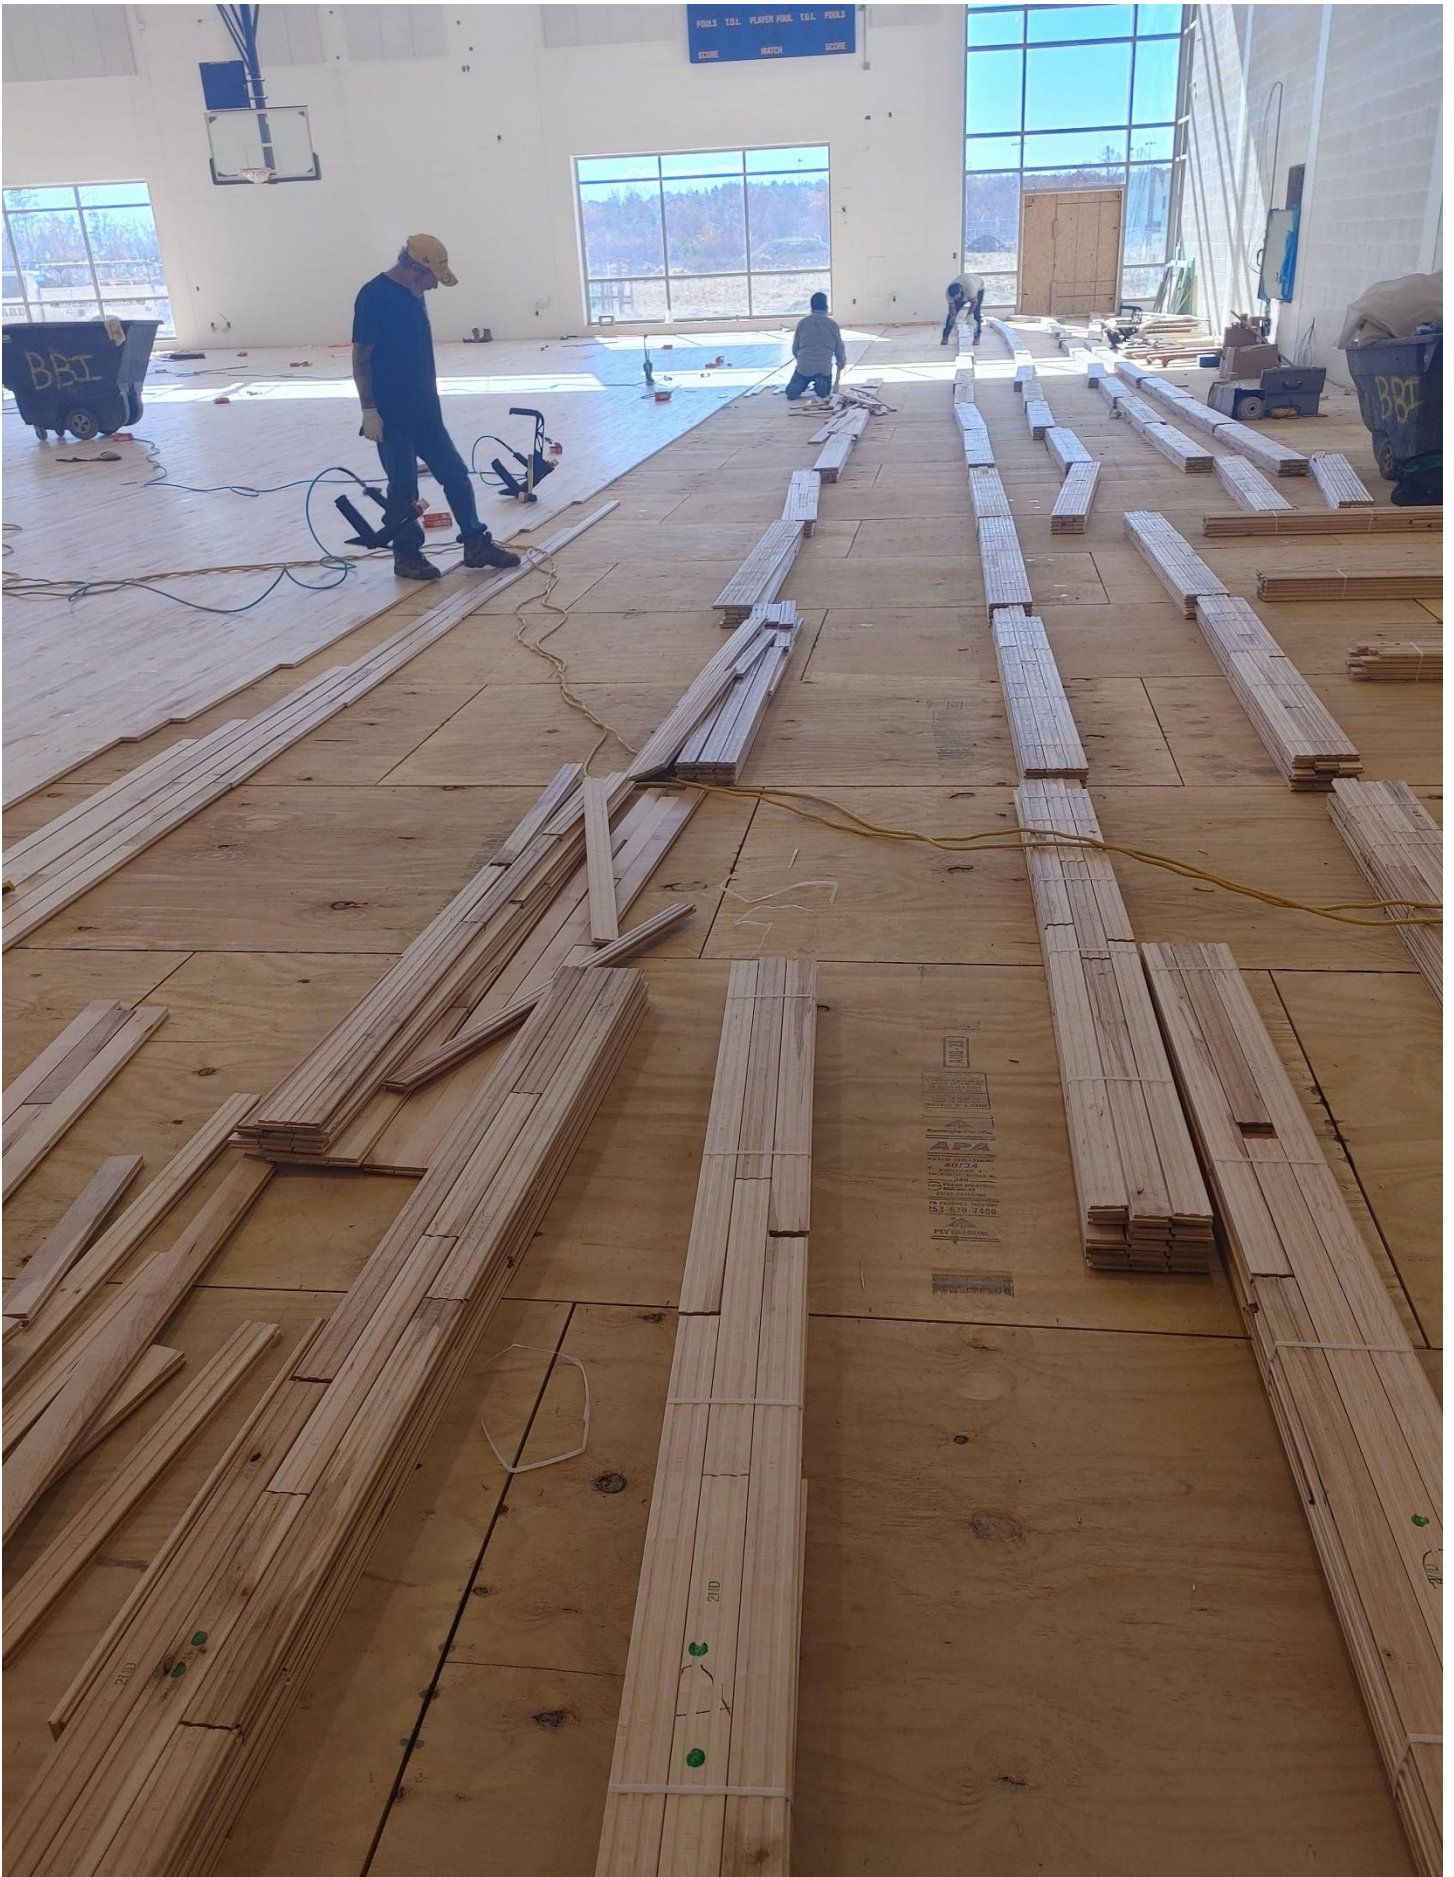


Photo 14 - Gym floor is being installed



Photo 15 – Preparing to set SF49B in Area C.

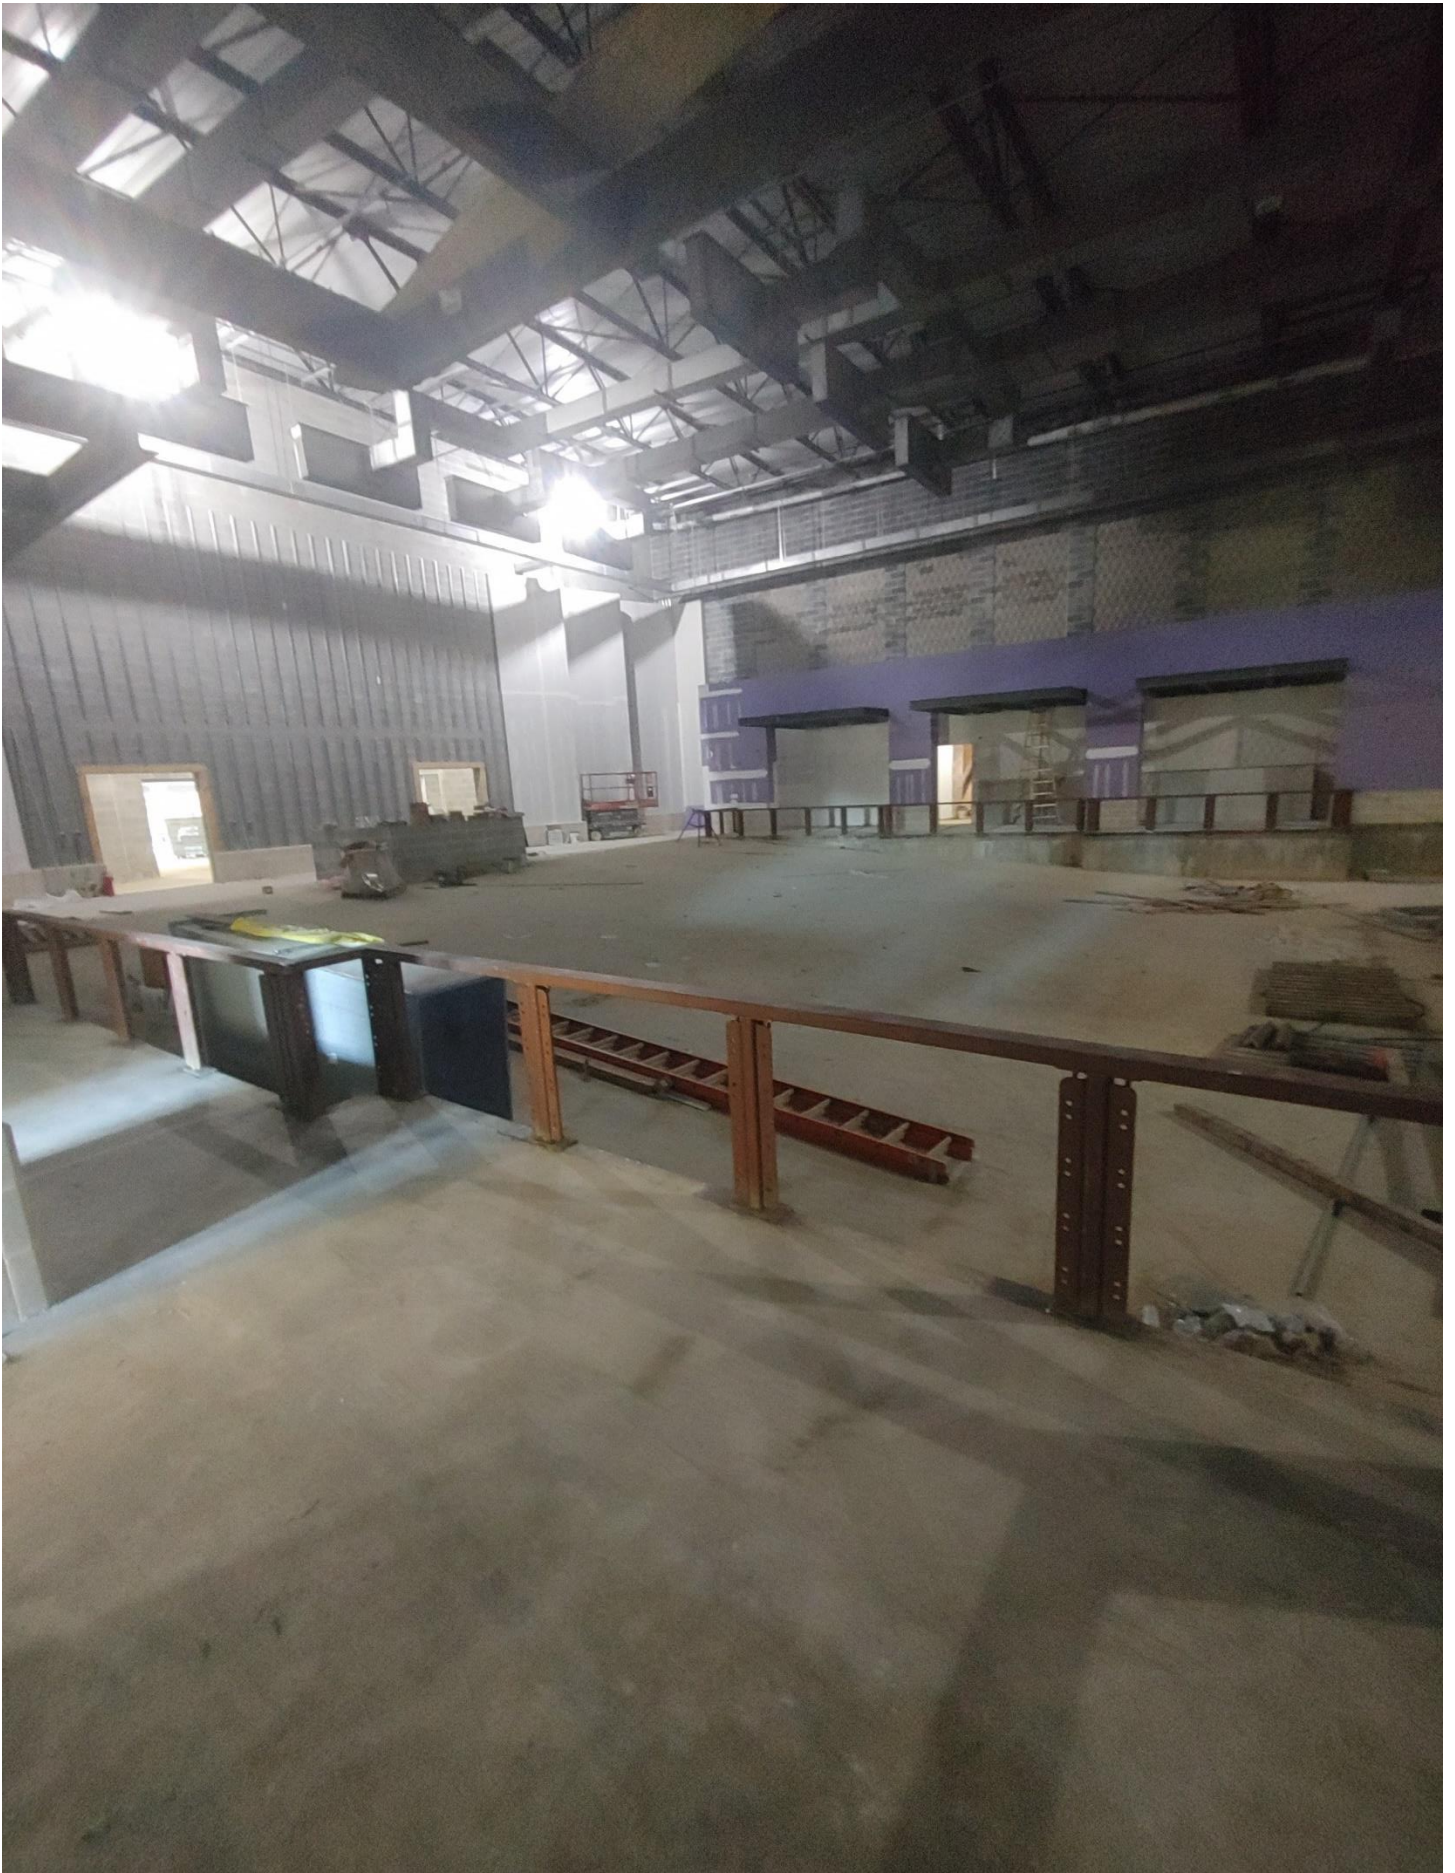


Photo 16 - Progress is being made in the Auditorium
