



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 12/10/2021
Weather: 54 degrees. Mostly Cloudy. High of 54 degrees today.
Hours Worked: 12/06/2021 – 13:30 – 16:30hrs (3hrs)

I arrived on site and noted that the Asphalt Paving crew was on site laying asphalt in the Northeast corner of the Student Parking Lot. The site is fairly empty this afternoon. I walked the site to observe what work was occurring.

Beuchert Excavation: Is on site working was working around the Retention Pond on the Northwest corner of the Bus Loop.

Industrial Concrete: I did not observe anyone on site during my visit.

J.D. Long, Masons: They are not on site today.

Hazzard Electric: They are on site working running electrical wiring and setting receptacles throughout the building.

Colonial Webb: I did not observe anyone on site.

Talley & Armstrong (Sub-Contractor of Beuchert): I did not observe anyone on site.

Weldon Steel: I did not observe anyone on site.

JP Construction: I did not observe anyone on site during my visit.

AAR Roofing: No one is on site today.

Tailored Foam: No one is here today.

FG & M: No one is on site today.

United Sprinkler: No one is on site.

CTSI: No one is on site to my knowledge.

M. L. Straight: I did not observe them on site today.

K-Plus: I did not observe anyone on site today during my visit.

AAM: They are installing Metal Panels on the West side of Area D.

Hodgemen: I did not observe anyone on site during my visit.

Deleware Elevator: No one was on site during either visit.

S&S Concrete Cutting Company: No one is on site today.

DES: There was a crew installing Cabinetry on the second floor or Area A.

Smith: No one is on site to my knowledge.

TJ Distributers, INC: No one was observed on site during my visit

Linear Surveyors: No one is on site today.

Hillis-Carnes: I did not observe anyone on site during my visit.

Conversations with Branch Builds: I met with John Farthro and Lee in Branch's office. I confirmed for John Farthro that the County has turned back on the 12" water line to the Town that feeds the School. It had been turned off for approximately a week.

Earlier in the week Todd had contacted me asking me if I was aware that the Sewage Pump station wiring requirements had changed. He said that the Electrician is saying that the two pumps require separate circuits to operate. He also said that originally the pumps called for a twenty amp circuit but now require a Thirty Amp Circuit. I told him that to my knowledge everything was installed according to the submittal that was distributed in May. Todd asked if I would contact the Engineer and verify if the pumps were to alternate operation or if one was purely a backup pump. I told him I would look into the matter and get back to him. I called Franklin Mechanical who confirmed that everything was installed in accordance with the Approved Submittal. I then contacted the Engineer who advised that the Pumps are to alternate operations and be controlled by the Control Panel and therefore should only require the one circuit. I reviewed the Submittal and it calls for a twenty Amp Circuit. I advised Todd of my finding and I am waiting to hear back from him if something is not right.

Yesterday, Norm Risavi Requested that I set up a Tour of the New High School for Monday, December 13, 2021 at 16:00hrs for the Board of Supervisors and Montross Town Council. I reached out to John yesterday and set up the Tour. John advised today that he, Lee and Cooper would be present to conduct the Tour.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report - 12/06/2021, 12/08/2021, 12/09/2021

Hillis-Carnes Grout Inspection/Compression Strength Test –

Hillis-Carnes Field Reports – 11/20/2021, 12/01/2021, 12/02/2021, 12/03/2021

Hillis-Carnes Bio Retention Pond Reports –

Submittals – #27 41 16.64-2.1, #27 41 16-1.0, #05 12 00-17.0

RFIs –

Patrick Byrne –

Alexes Lee – Update Contingency 12/06/2021

Tara Delaney – Change Order #14 12/08/2021 Accepted

Change Order/PCOs/Pay App –

Weekly Submittal Status Report: 12/10/2021

Weekly RFI Status Update – 12/10/2021

Weekly Daily Log Summary – 12/10/2021

PCO Log – 12/10/2021



Photo 1 - Asphalt is being laid in the Northeast corner of the Student Parking Lot.



Photo 2 - Main Entrance



Photo 3 - Cabinetry has been installed in the Administrative Area.



Photo 4 - Progress continues on the Grand Staircase

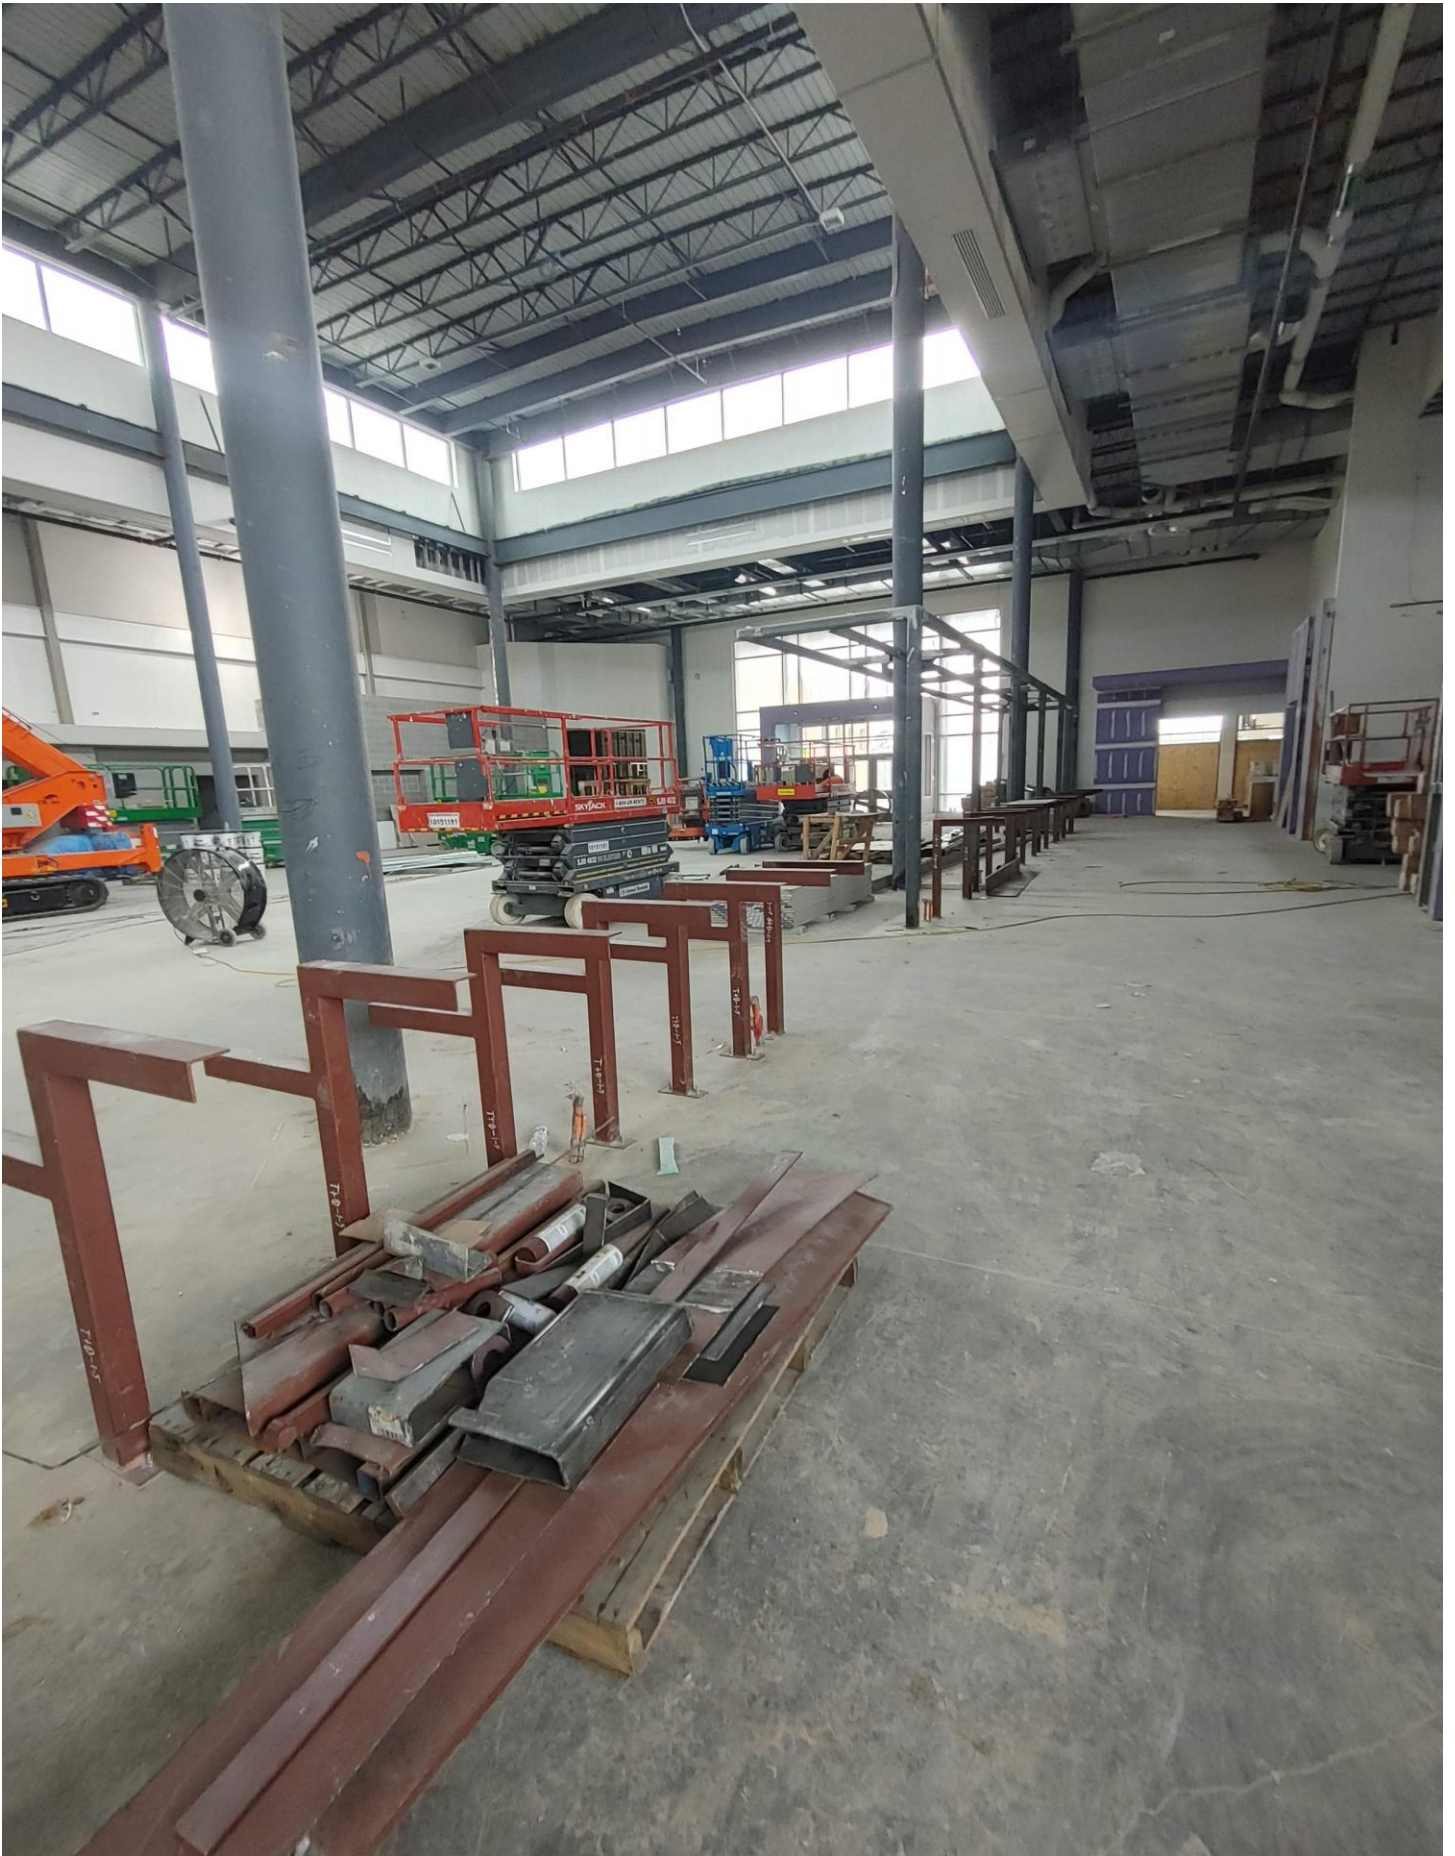


Photo 5 - the Two-tiered Bar frame has been installed in Area C

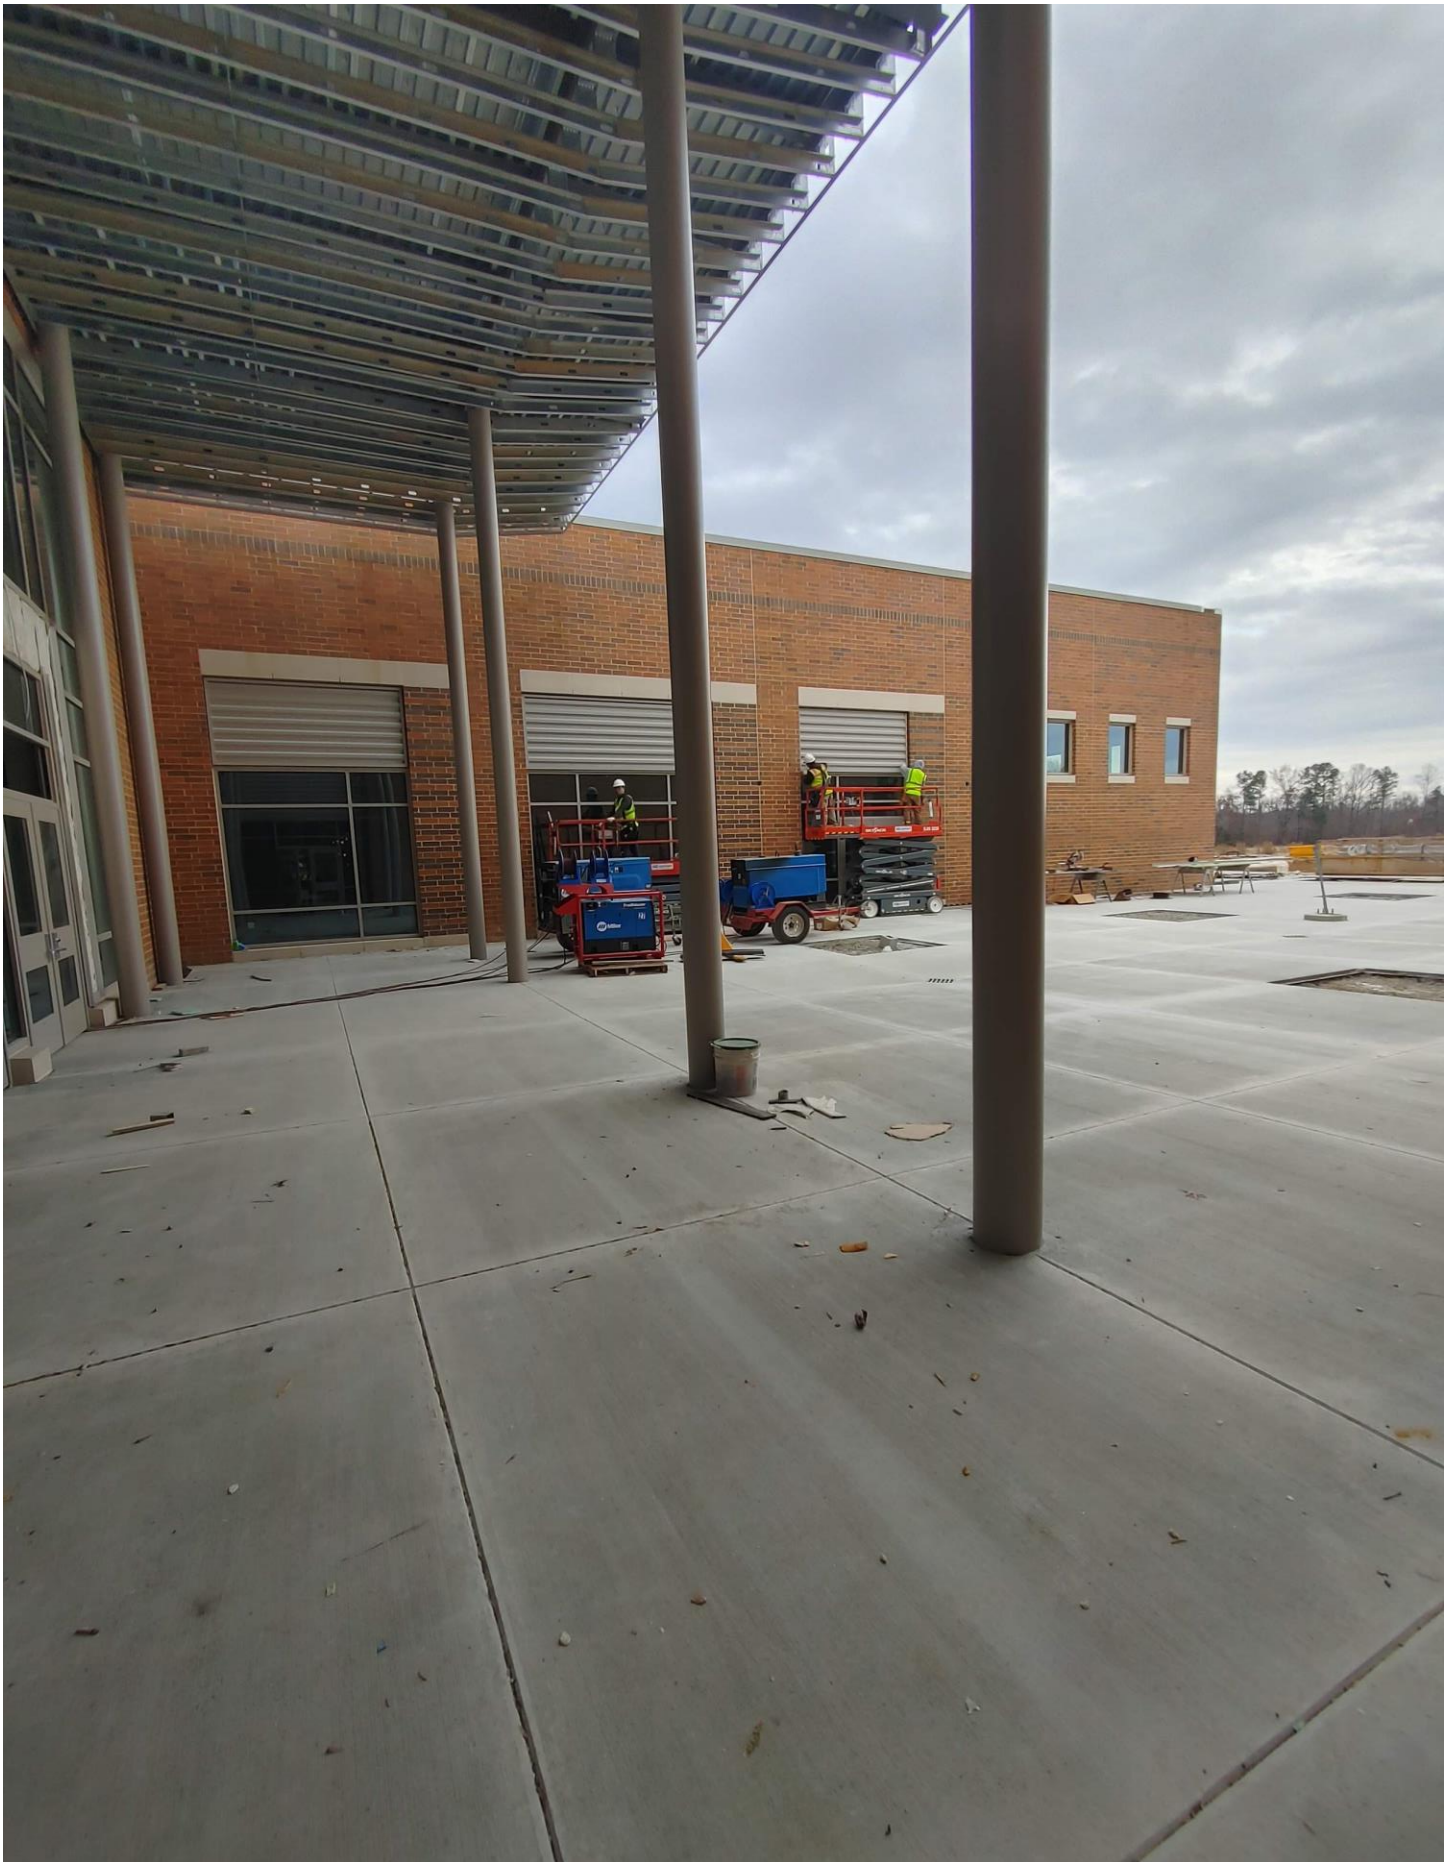


Photo 6 - Metal Panels are being installed on the Westside of Area E

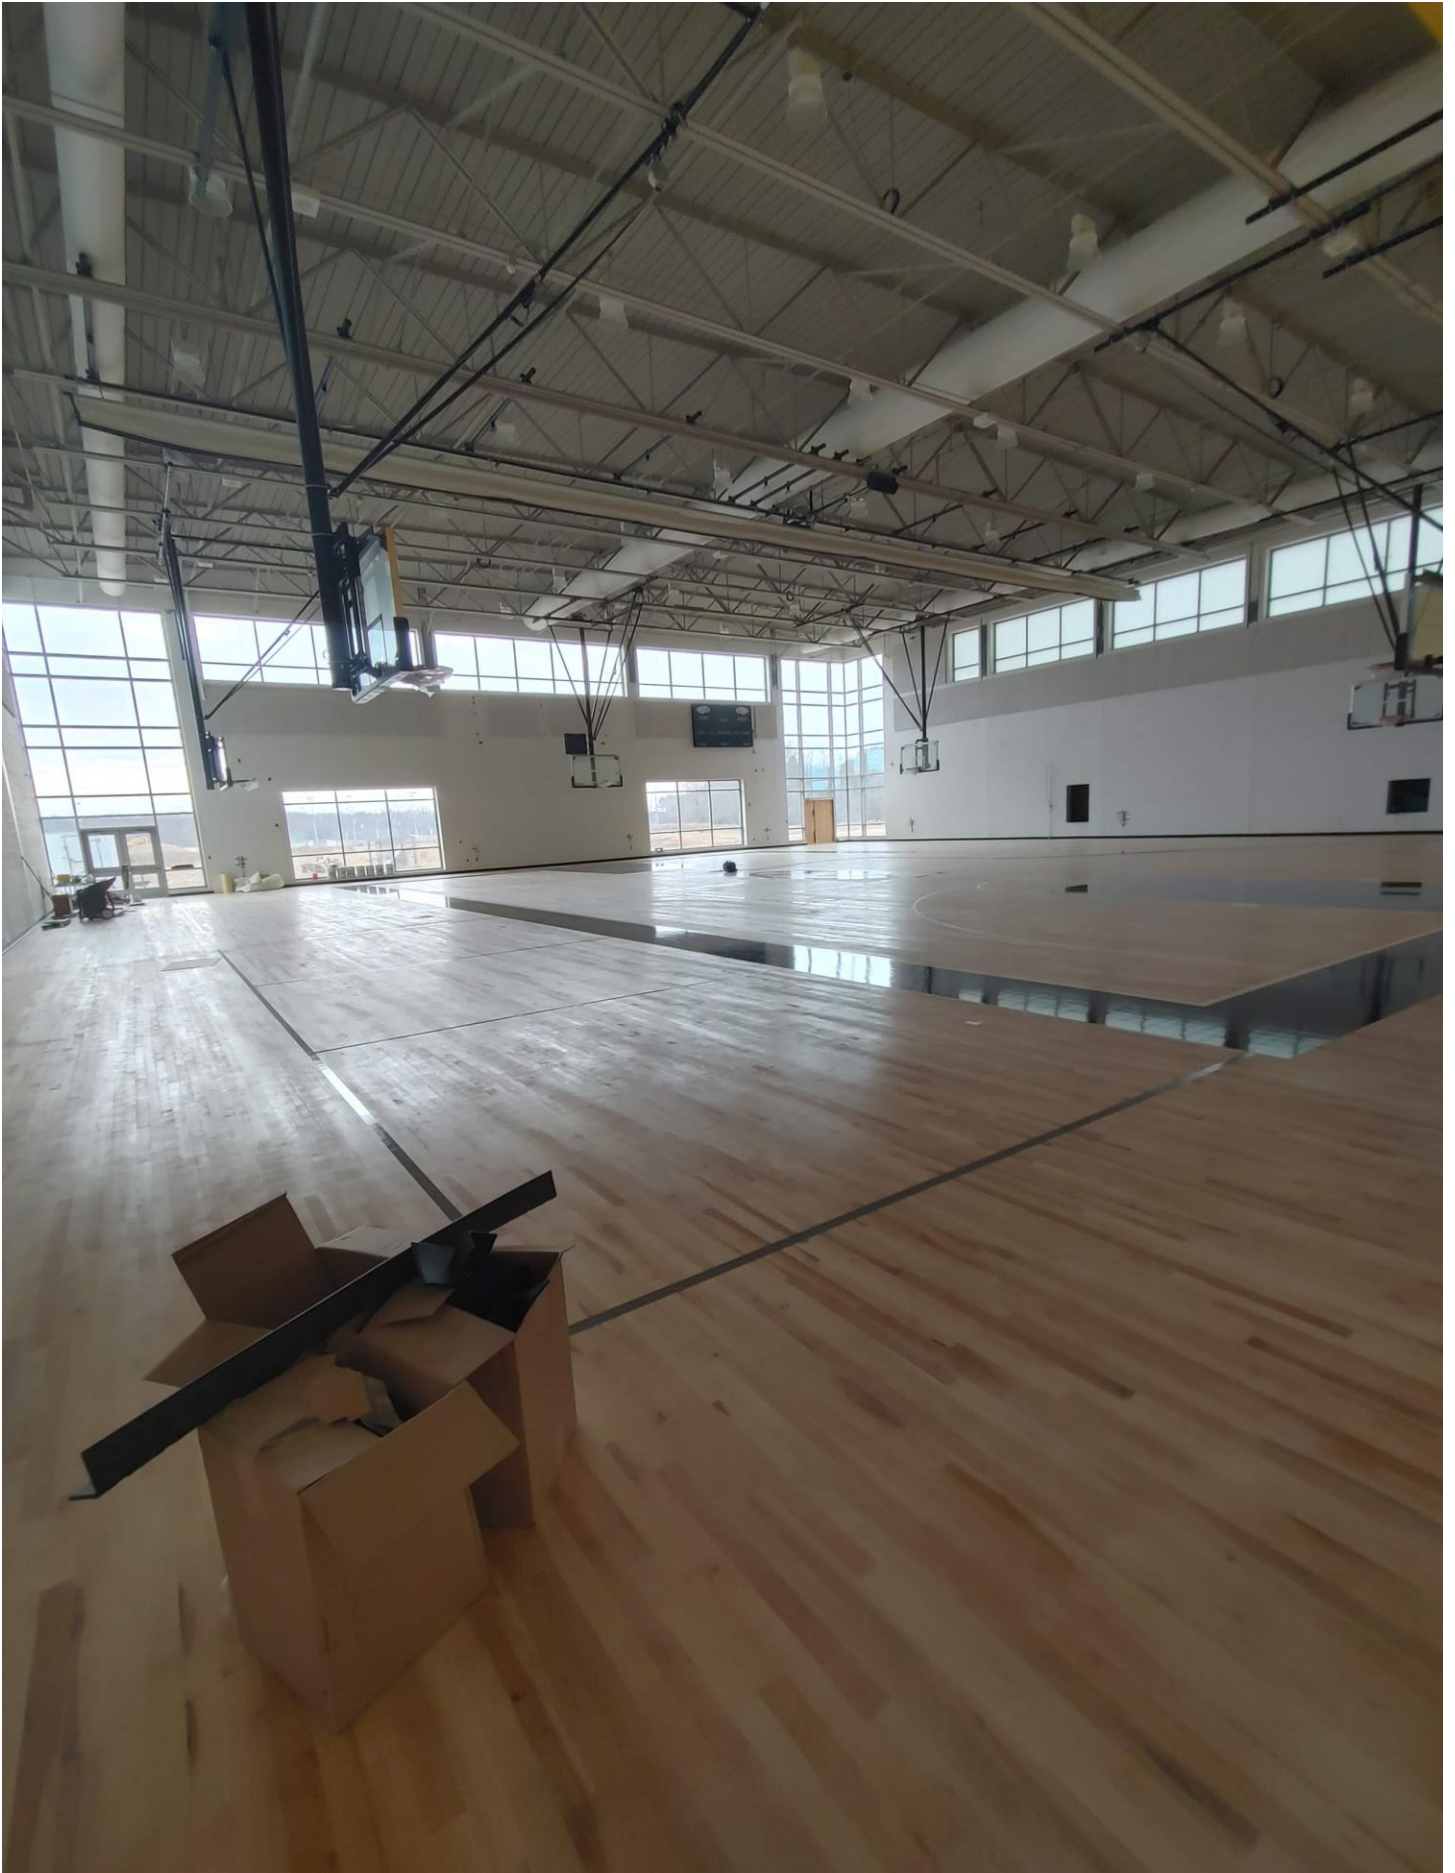


Photo 7 - Progress continues on the Gymnasium Floor



Photo 8 - Railing have been installed in Stairwell #1

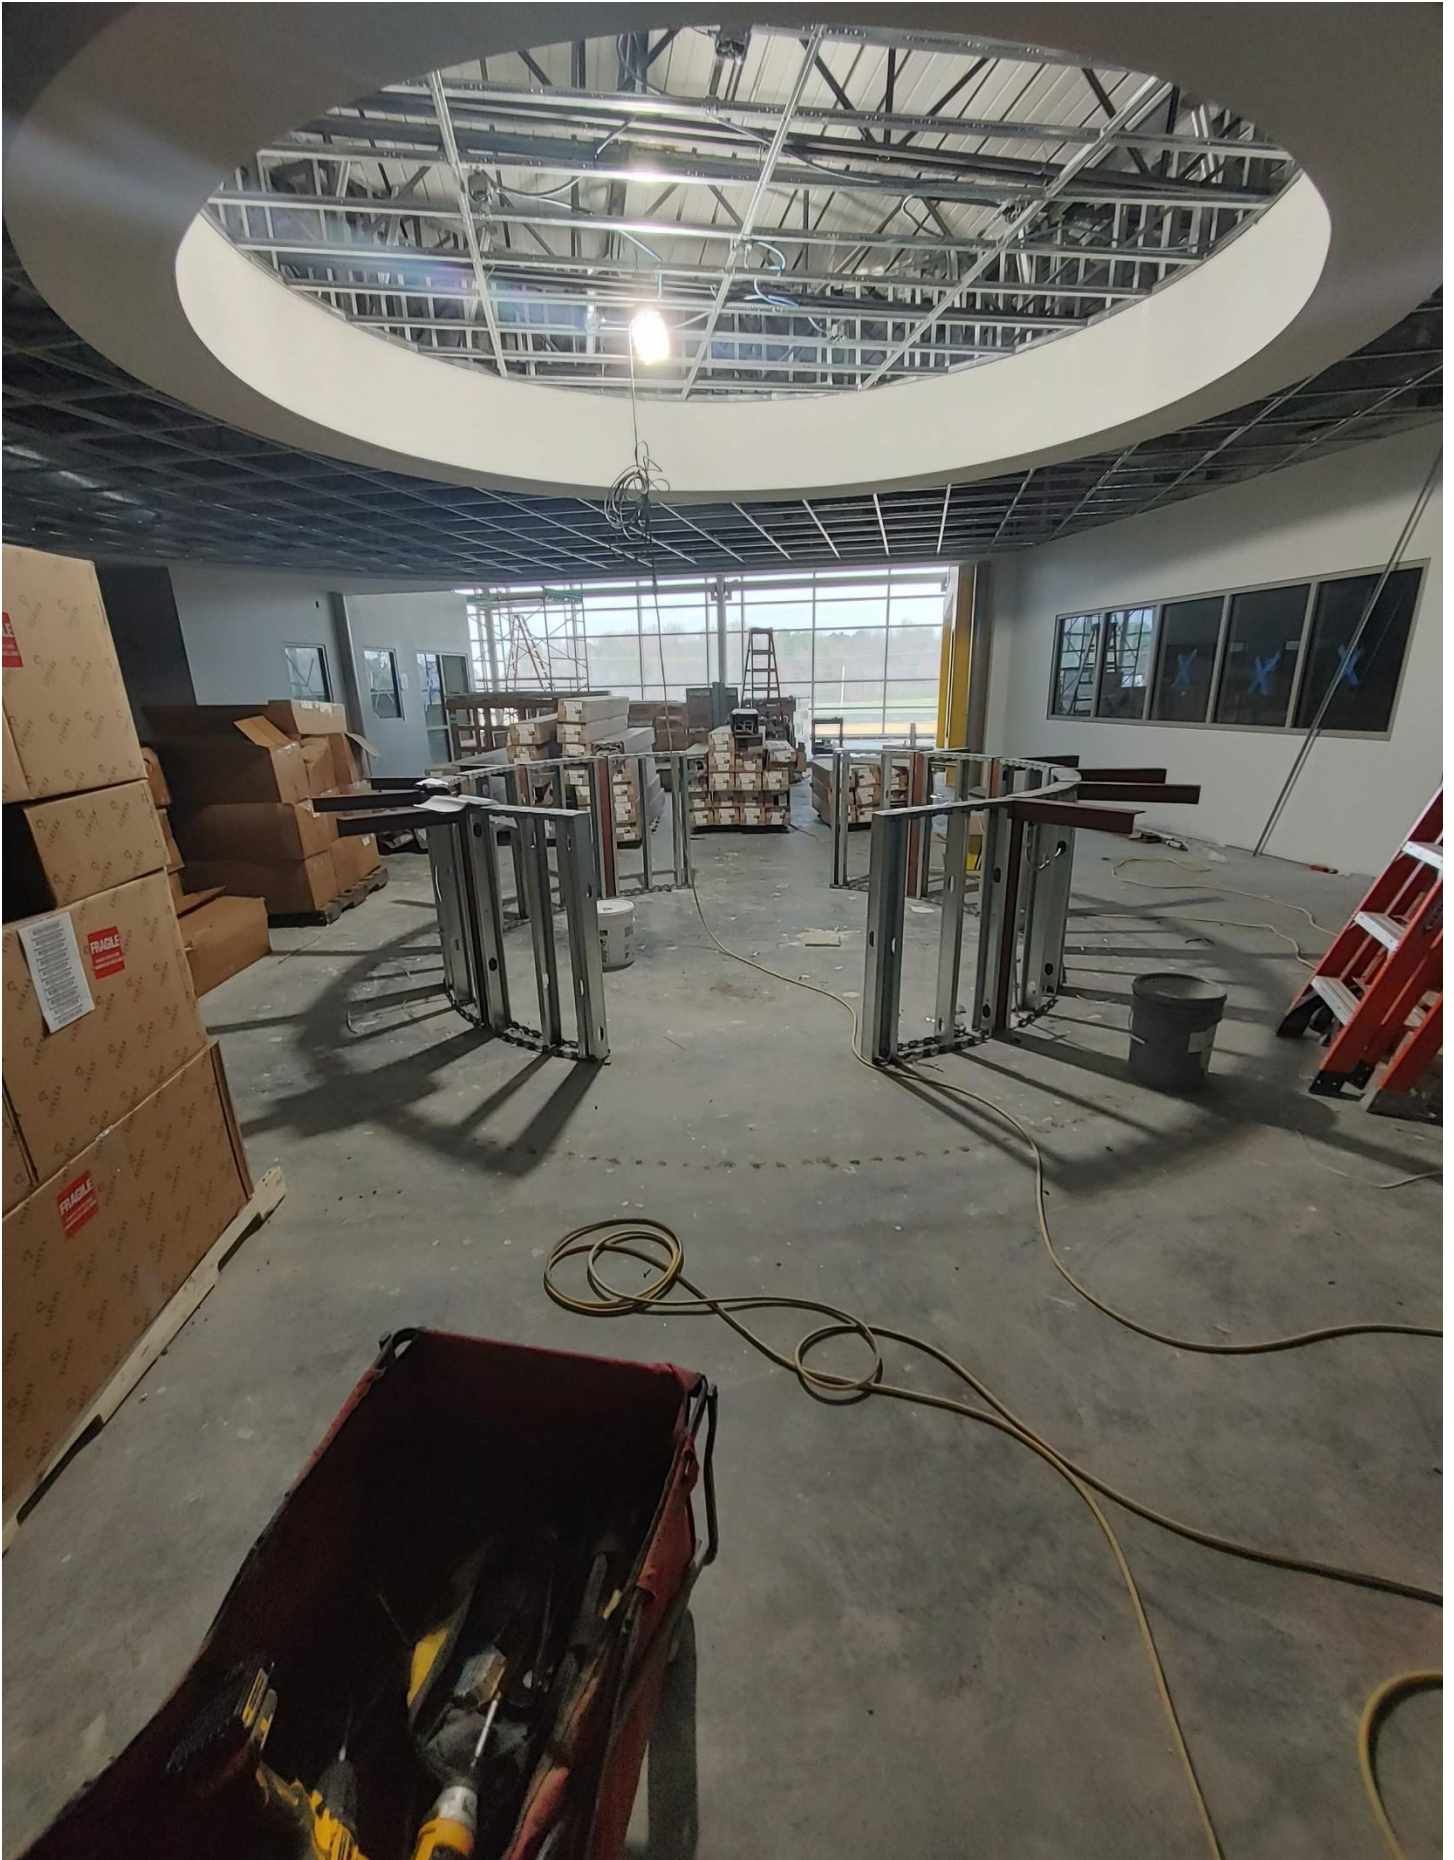


Photo 9 - Curved Power Bar in the Innovations Commons area of Area A is being constructed.
