



**COMMONWEALTH  
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West

Aylett, Virginia 23009

Phone: 804-761-4248

FrazierConsulting@gmail.com

Licensed Class A - RBC/CBC

DEPOR # 2705169996

EIN# 83-1821991

**FIELD REPORT**

**WESTMORELAND COUNTY HIGH SCHOOL**

Date: 12/15/2021  
Weather: 47 degrees. Partly Sunny. High of 57 degrees today.  
Hours Worked: 09:00 – 12:00hrs (3hrs)

I arrived on site and noted that the Asphalt Paving crew were on site and laying asphalt where the driveway ties into County Park Drive. Mark Friedenstine, VDOT inspector asked me to keep an eye on this connection to ensure that the existing asphalt is milled at the connection. I called Mark and he indicated that his concern is to ensure that the existing Asphalt is milled when the topping layer of Asphalt is applied. They are currently only laying the Base Asphalt.

**Beuchert Excavation:** Is on site working was working around the Retention Pond on the Northeast corner of the Bus Loop. Asphalt crew is currently laying Asphalt on the Drive Lane in front of the School.

**Industrial Concrete:** I did not observe anyone on site during my visit.

**J.D. Long, Masons:** They are not on site today.

**Hazzard Electric:** They are on site working running electrical wiring and setting receptacles throughout the building. One man is working on Light Pole bases at the Northeast corner of the property.

**Colonial Webb:** They are on site today working on various mechanical items.

**Talley & Armstrong (Sub-Contractor of Beuchert):** I did not observe anyone on site.

**Weldon Steel:** I did not observe anyone on site.

**JP Construction:** They are on site hanging and finishing Sheetrock and installing corner bead.

**AAR Roofing:** No one is on site today.

**Tailored Foam:** No one is here today.

**FG & M:** No one is on site today.

**United Sprinkler:** I noted one man on site running sprinkler pipe in Area C.

**CTSI:** They are here today pulling low voltage wiring.

**M. L. Straight:** They are here today painting in Stairwell #2 and on the 2<sup>nd</sup> floor of Area B.

**K-Plus:** I did not observe anyone on site today during my visit.

**AAM:** I did not observe anyone on site during my visit

**Hodgemen:** I did not observe anyone on site during my visit.

**Deleware Elevator:** No one was on site during either visit.

**S&S Concrete Cutting Company:** No one is on site today.

**DES:** I did not observe anyone on site today.

**Smith:** No one is on site to my knowledge.

**TJ Distributers, INC:** No one was observed on site during my visit

**Linear Surveyors:** No one is on site today.

**Hillis-Carnes:** I did not observe anyone on site during my visit.

**Conversations with Branch Builds:** I met with John Farthro, Cooper and Jake in Branch's office. I told John that the County had received a few complaints from some of the neighbors about trash that had blown off site across County Park Drive. John said he would have a crew police the area.

Branch would like to temporarily use County Park Drive as an entrance for workers to access the site while the Bus Loop is being paved. So, Lee and I walked the area to identify any existing damage to either the Asphalt or curb and gutter. Lee took multiple pictures of imperfections, indentations or damage to the existing asphalt and gutter pan.

On Monday, December 13<sup>th</sup> I attended a Tour of the New High School with Norm Risavi, and Members of the Board of Supervisors, Montross Town Council and the Industrial Development Authority.

**Compliance with Contract Documents:** No noted discrepancies.

**DEQ Reports:** A re-inspection of the site was conducted on November 29<sup>th</sup>, 2021.

**Reviewed emails:**

**Hillis-Carnes Concrete Break Report** - 12/10/2021, 12/14/2021

**Hillis-Carnes Grout Inspection/Compression Strength Test** –

**Hillis-Carnes Field Reports** – 12/09/2021, #12/10/2021, 12/13/2021

**Hillis-Carnes Bio Retention Pond Reports** –

**Submittals** – #07 84 46-2.1, #11 61 43-10.0, #26 22 00-3.0

**RFIs** – #344, #347, #354, #359

**Patrick Byrne** –

**Alexes Lee** –

**Tara Delaney** –

**Change Order/PCOs/Pay App** –

**Weekly Submittal Status Report:**  
**Weekly RFI Status Update –**  
**Weekly Daily Log Summary –**  
**PCO Log –**




*Photo 1 - Base Asphalt is being tied into County Park Drive*



*Photo 2 - Bio Retention Pond on the Northeast side of High School*



*Photo 3 - Sheetrock is being finished in Area C*

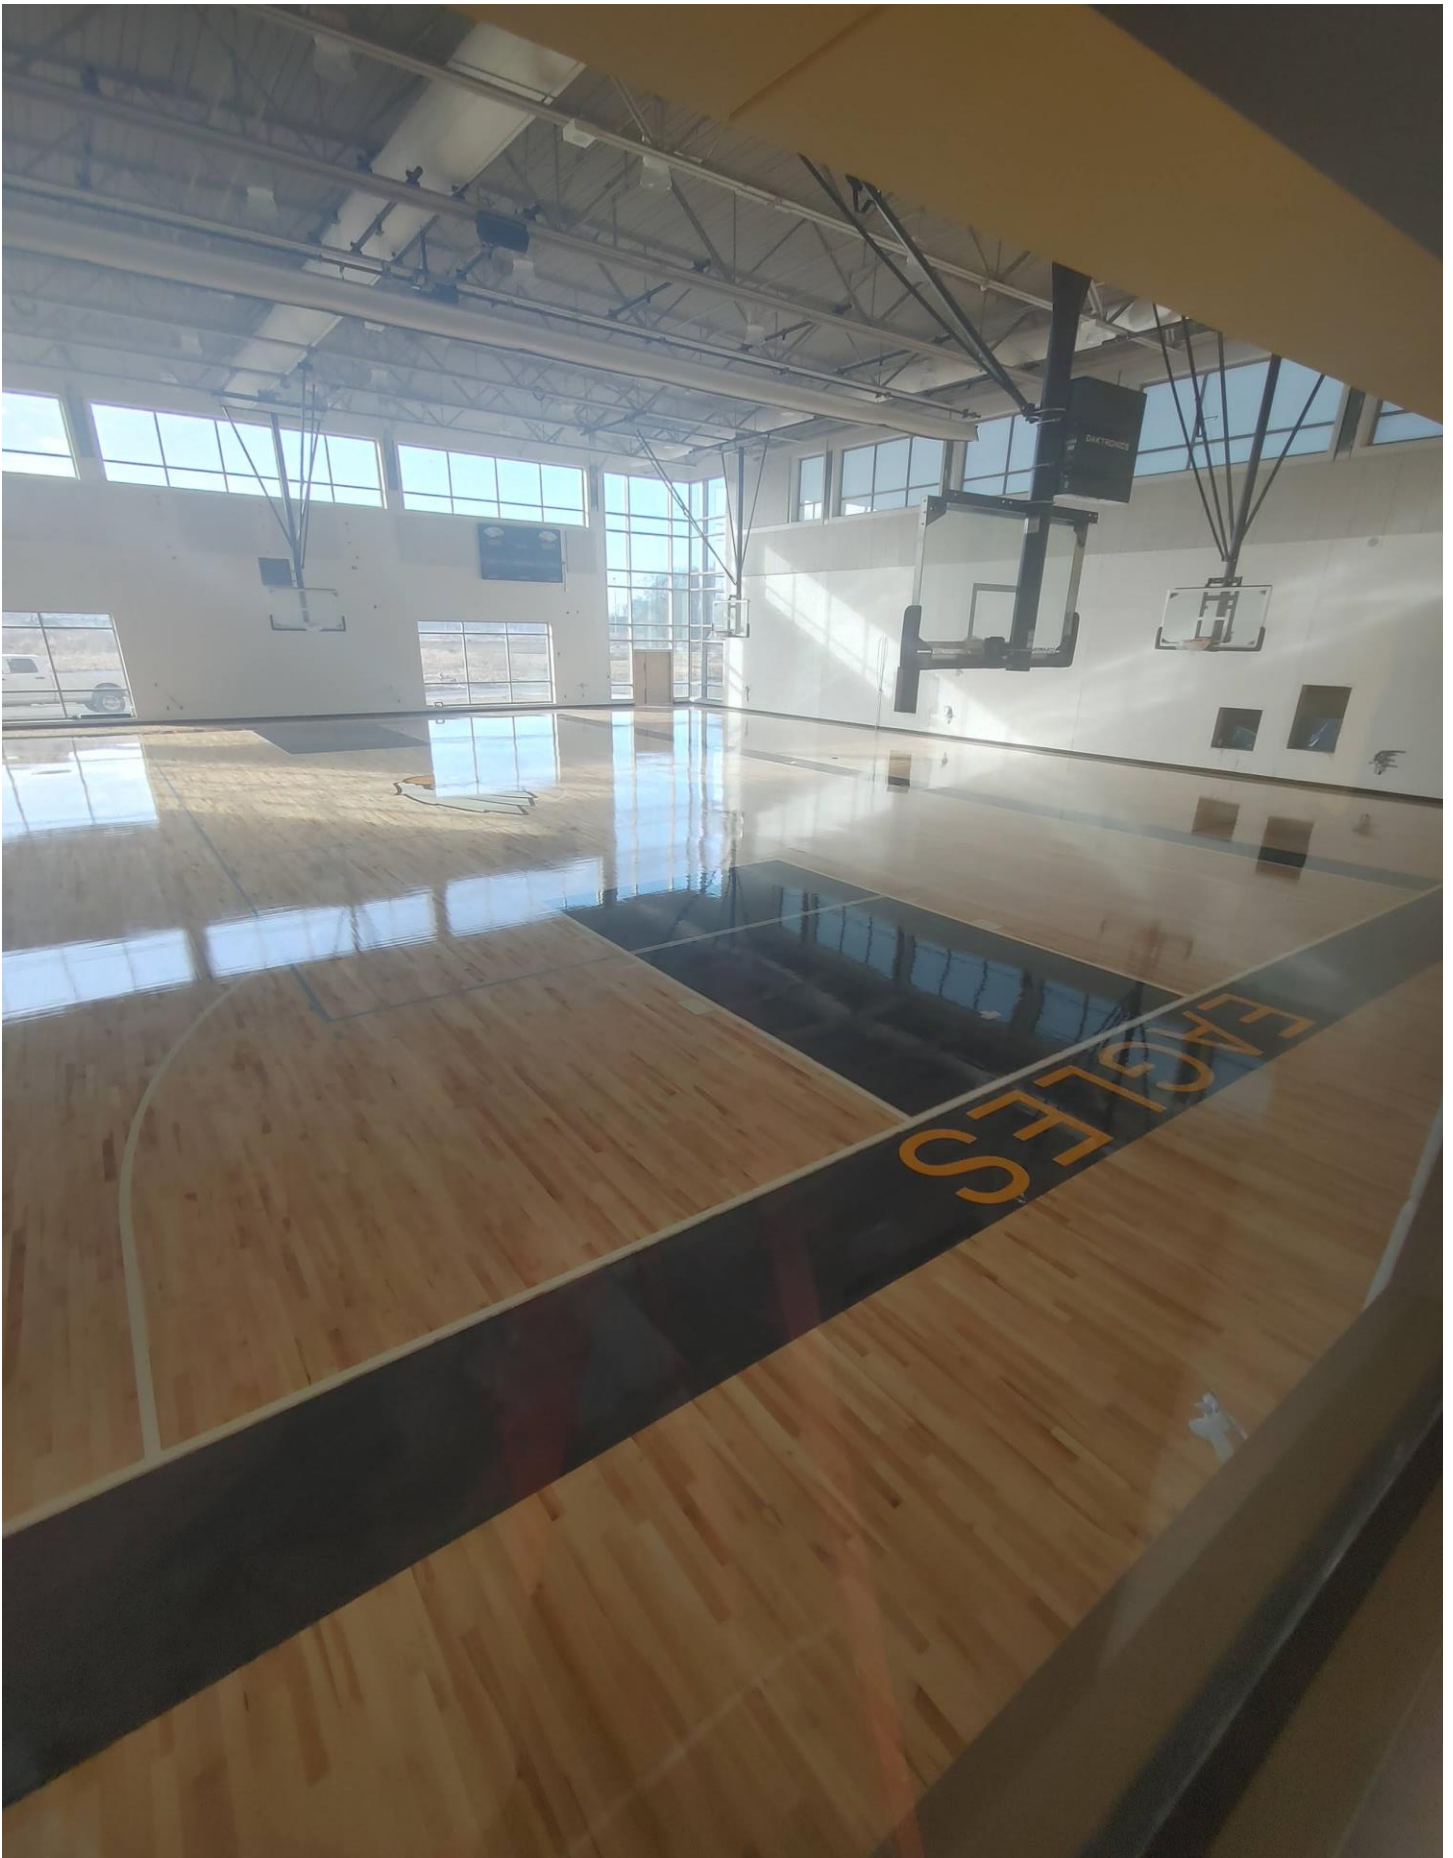

*Photo 4 - Gymnasium Floor has been completed*

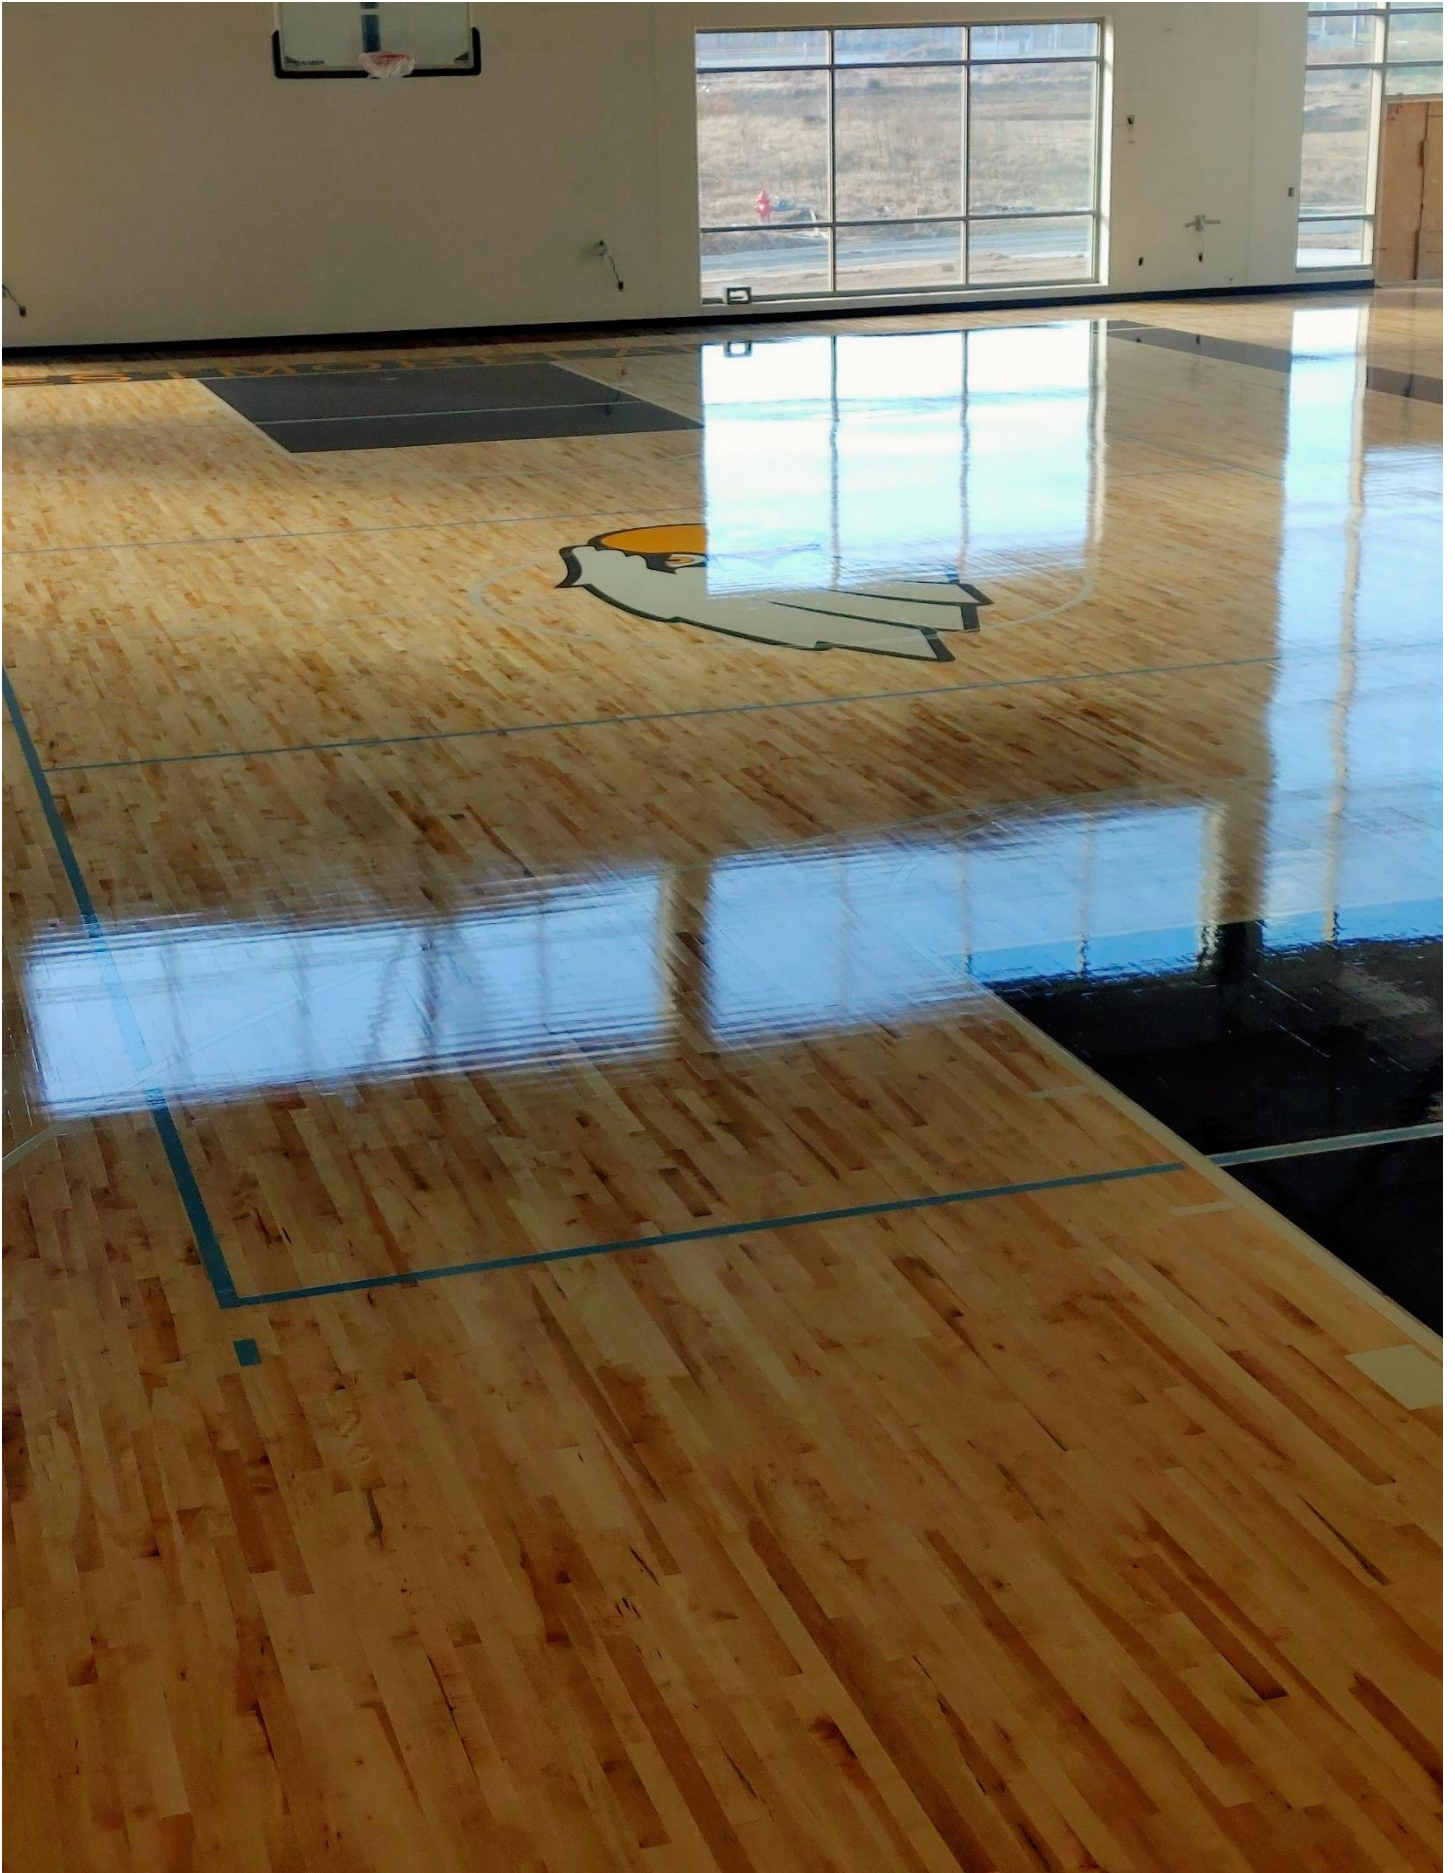


Photo 5 - Eagle Logo in center of floor.





Photo 6 - Ceilings are being hung in locker rooms.



Photo 7 - Work is progressing on the Grand Staircase.



Photo 8 - Main Drive Lane in front of the school is receiving the Base Layer of Asphalt.



Photo 9 - Northwest Student Parking Lot.



Photo 10 - West side of site



Photo 11 - Student Entrance Area



Photo 12 - Roof top units above Kitchen and Mechanical room



Photo 13 - East side of the site
