



**COMMONWEALTH
BUILDING SOLUTIONS, LLC**

336 Cherry Hill Circle West
Aylett, Virginia 23009
Phone: 804-761-4248
FrazierConsulting@gmail.com
Licensed Class A - RBC/CBC
DEPOR # 2705169996
EIN# 83-1821991

FIELD REPORT

WESTMORELAND COUNTY HIGH SCHOOL

Date: 12/22/2021
Weather: 45 degrees. Sunny. High of 48 degrees today.
Hours Worked: 10:30 – 12:30hrs (2hrs)

I did not attend the last Progress Meeting on did not know that today's Progress Meeting had been canceled. I went to the County's Office Building and everyone had taken off. So, I went to the High School and John Fartro told me it had been canceled.

Beuchert Excavation: Is on site working was working around the Retention Pond on the Northeast corner of the Bus Loop grading the shoulder.

Hazzard Electric: They are on site working throughout the building.

Colonial Webb: They are on site today working on various mechanical items.

Talley & Armstrong (Sub-Contractor of Beuchert): Are working on Sidewalks in front of the Building.

Weldon Steel: They are on site working on the Grand Staircase.

United Sprinkler: I noted one man on site running sprinkler pipe in Area C.

K-Plus: Is on site today.

Hillis-Carnes: I did not observe anyone on site during my visit.

Fence Company: There is a crew on site today installing the Fence between the Bus Parking Area and the BMP. They will also be installing Bollard in various areas around the site.

Conversations with Branch Builds: I met with John Farthro, Cooper and Lee during my visit. I asked Cooper about where we stood on resolving the Deficiency List sent out by Hillis-Carnes back in mid-November. Cooper said that Branch is slowly dwindling down the list and said that many of the items have been resolved.

In my previous report I had asked John Farthro if Branch could perform a cleanup of the debris that had blown off site across County Park Drive. Branch completed that cleanup the very same day.

The Base layer of asphalt has been laid.

Compliance with Contract Documents: No noted discrepancies.

DEQ Reports: A re-inspection of the site was conducted on November 29th, 2021.

Reviewed emails:

Hillis-Carnes Concrete Break Report - 12/16/2021, 12/17/2021,

Hillis-Carnes Grout Inspection/Compression Strength Test – 12/20/2021, 12/21/2021

Hillis-Carnes Field Reports – 12/15/2021, 12/16/2021, 12/17/2021, 12/20/2021

Hillis-Carnes Bio Retention Pond Reports –

Submittals –

RFIs – #342, #356, #357

Patrick Byrne –

Alexes Lee –

Tara Delaney –

Change Order/PCOs/Pay App –

Weekly Submittal Status Report: 12/17/2021

Weekly RFI Status Update – 12/17/2021

Weekly Daily Log Summary – 12/17/2021

PCO Log – 12/17/2021



Photo 1 - Work is progressing on the Grand Staircase



Photo 2 - Bleachers are being erected in the Gym.

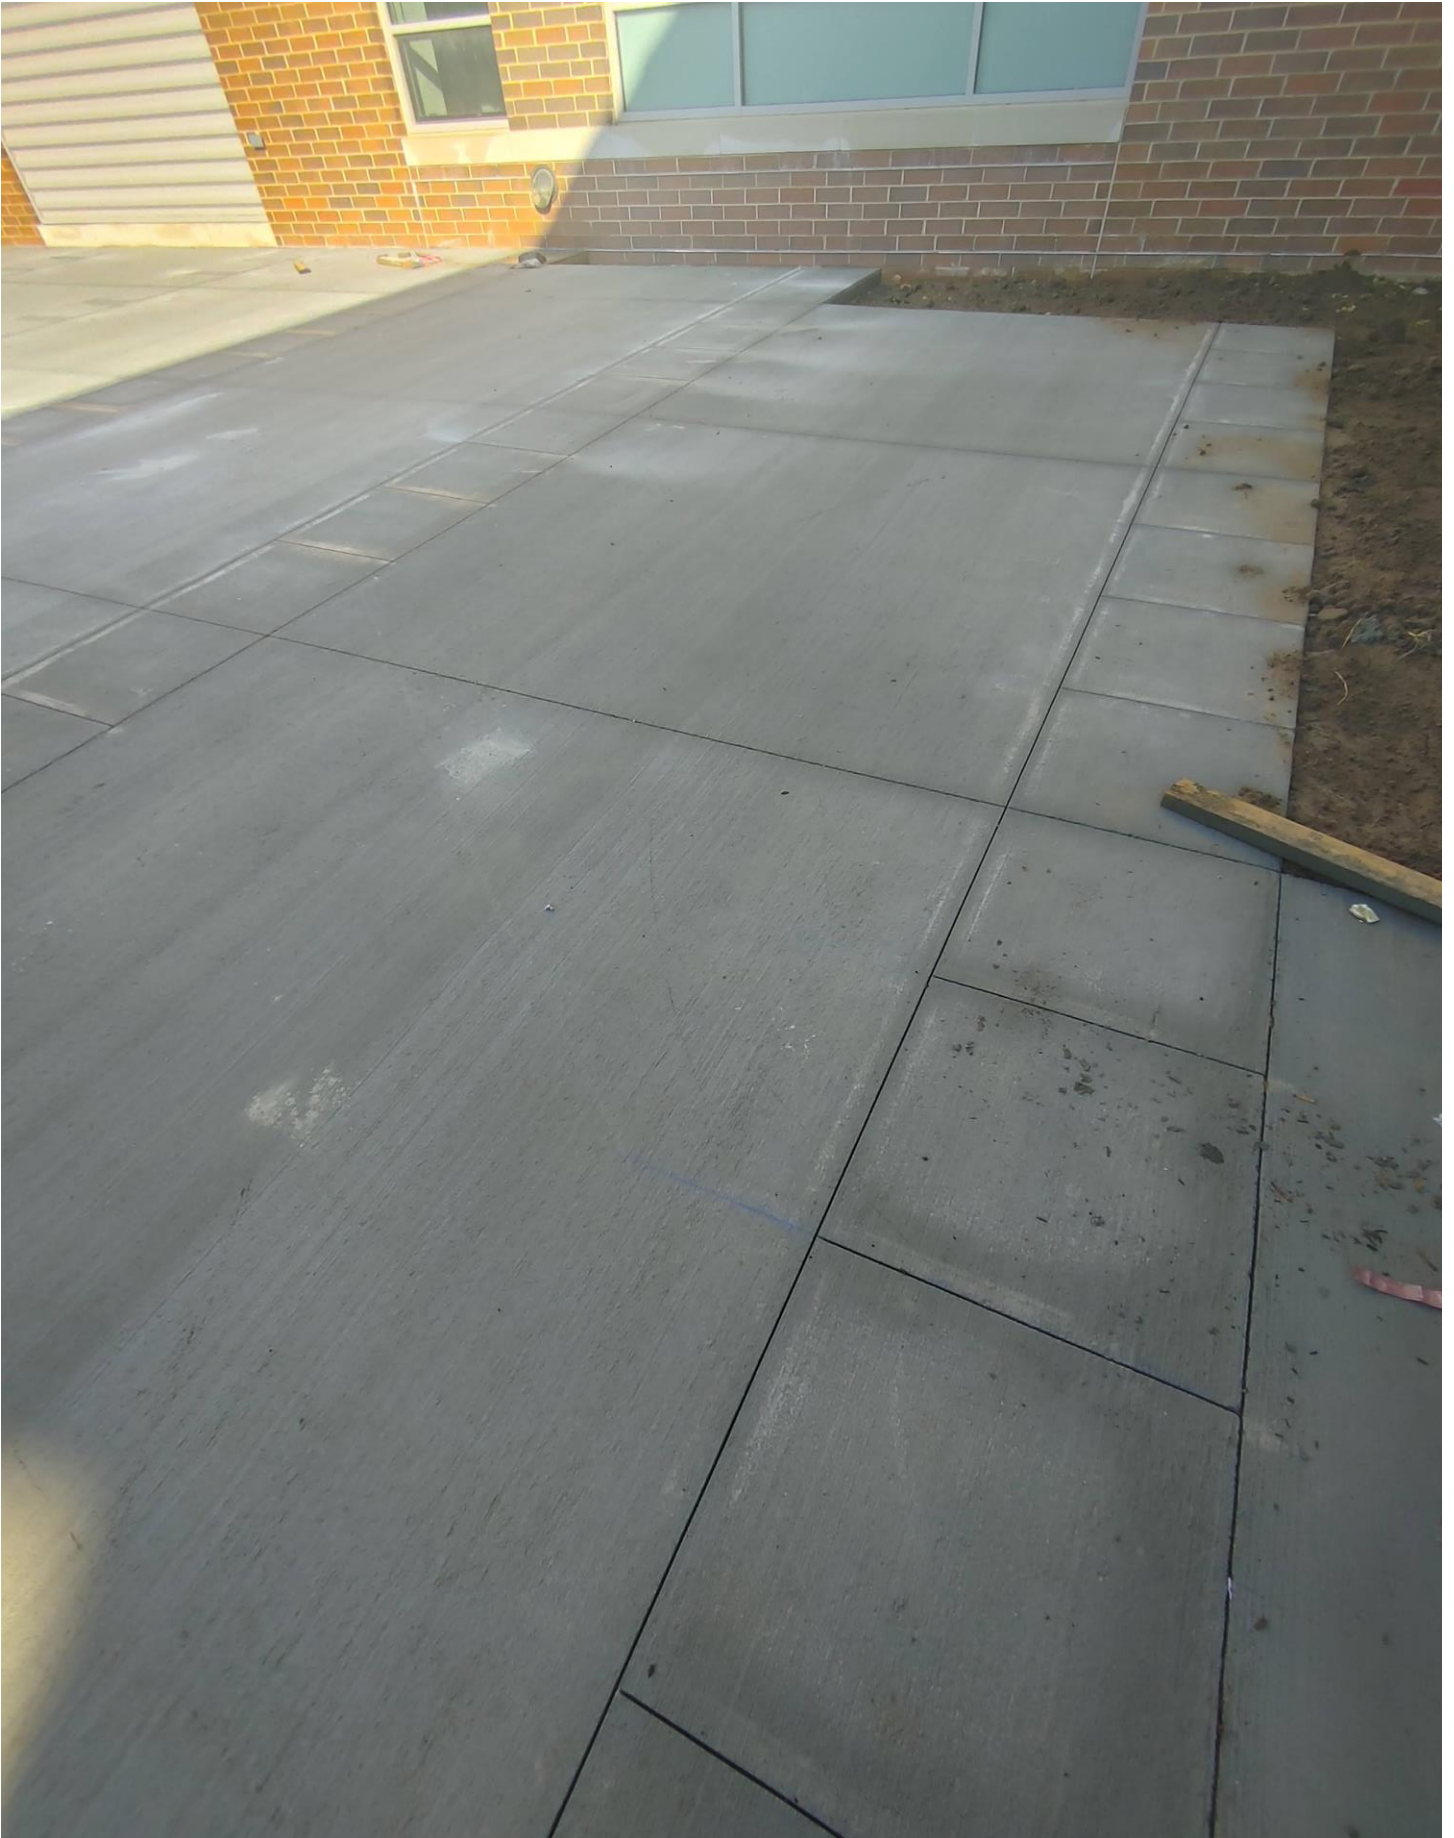


Photo 3 - Concrete is being Scored between Zone #3 & #5



Photo 4 - Concrete is being Scored



Photo 5 - Fence Posts are being installed



Photo 6 - Fence Posts are being installed between the Bus Parking Area and the BMP



Photo 7 - Bus Loop Road



Photo 8 - South side of the School.
